

**BACK TO
METAL**

WHY THIS BOOK EXISTS

YOU ARE ALLOWED TO RUN YOUR OWN COMPUTERS

A generation of engineers has now been trained to believe that owning a server is a kind of professional failure. It is not. It is a trade, and like every trade it has terms: you take on hardware, capacity and a pager, and in exchange you stop paying a margin on every byte you move and every hour you idle. For a company spending real money on one cloud, that trade is usually worth making, and the arithmetic is not close.

What has been missing is not the argument. It is a plan short enough to finish. Repatriation is written about as a decision and executed as a crisis, which is why so many attempts stall halfway, with two platforms live and nobody able to say whether it is going well. This is the other thing: 20 Moves, in five stages, each one a single job with a stated cutover, a stated risk and a rollback that works. An earlier edition of this book had a hundred and twenty-two of them and took four years. Nobody has four years.

It is honest about the parts that do not pay. One whole Move ends by telling you to keep paying somebody else, because a content network, denial-of-service scrubbing and outbound email are three things you will not beat on your own, and a book that pretends otherwise is selling something. Another gives you permission to read three Moves, do the arithmetic, and stop. The point was never to own everything. It was to own the parts where ownership is cheaper, faster and yours.

Which is why the whole thing is **open source**. Every Move, the typesetter that turns them into this book, and the site that publishes them are yours: the text under Creative Commons, the software under the MIT licence, all of it at github.com/OneUptime/back-to-metal. Correct it, extend it, add the services your own estate actually runs. Infrastructure knowledge this practical should not sit behind a consulting invoice.

BACK TO METAL

How a company leaves the cloud, in twenty moves

Nawaz Dhanda

BY THE MAKERS OF ONEUPTIME • [ONEUPTIME.COM](https://oneuptime.com)

HACKERBAY • [HACKERBAY.IO](https://hackerbay.io)

BACK TO METAL

How a company leaves the cloud, in twenty moves

Copyright © 2026 Nawaz Dhandala

Published by HackerBay, HackerBay.io

The text of this book, including every Move, is licensed under the Creative Commons Attribution 4.0 International licence. You may share and adapt it, including commercially, provided you give credit. The software that typesets this book is licensed separately under the MIT licence. Both are at github.com/OneUptime/back-to-metal.

The right of Nawaz Dhandala to be identified as the author of this work has been asserted in accordance with the Copyright, Designs and Patents Act 1988.

First edition, 2026. Version 4.1.1.

Every runbook in this book changes production infrastructure, and several of them move data that cannot be recreated. Read the Rollback section before the first step of any Move, take a backup you have restored at least once, and rehearse against a copy. Prices, service names and product behaviour are those the author observed while writing and will drift; the figures in each Move are illustrative of the shape of a saving, not a quotation. Nothing here is legal, financial, security or compliance advice. You remain responsible for your own systems, your own data and your own obligations to the people whose data it is.

Disclosure: the author founded OneUptime, which this book recommends for alerting, on-call, incidents and status pages. It is recommended because it is Apache-2.0 licensed, self-hostable, and does in one place what that Move would otherwise ask you to assemble from four separate tools. The alternatives named beside it are real ones, and a reader who prefers them loses nothing else in this book.

Set in Archivo, drawn by Omnibus-Type, and JetBrains Mono, drawn by Philipp Nurullin and Konstantin Bulenkov. Both are licensed under the SIL Open Font License.

backtometal.hackerbay.io

MANY MOVES, NOT ONE MIGRATION

The reason leaving the cloud fails is almost never that the technology did not work. It is that it was attempted as one decision, executed as one project, and abandoned somewhere in the middle with two platforms running and nobody able to say whether it was going well.

This book takes the opposite shape. It is 20 Moves, in five stages. Each is one job with a stated cutover, a stated risk and a rollback that has been thought about. Each can be done on a Tuesday and undone on a Wednesday. You can stop after any of them and still be in a coherent place, which is the only property that matters in a project measured in quarters.


It is deliberately small. The first edition had a hundred and twenty-two Moves and, computed from its own files, 975 person-days and four and a half years. That was correct and useless. This is 80 person-days and about 32 weeks for two people, most of it hardware lead time rather than work. Hiring does not shorten it.

They are ordered so that a reader who starts at Move 01 and works forward has, by construction, met every prerequisite of the Move in front of them. That is not a stylistic choice; the build refuses to compile a book where it does not hold.

Every Move carries all three clouds. The job is the same whether you are leaving AWS, Google Cloud or Azure — what differs is the extraction, so each Move opens with three lines naming the real service on each provider and the one thing that is different there.

Move 04 concludes that you should keep paying somebody else for three things. A content delivery network, scrubbing capacity at the edge and outbound email are businesses other people run better than you will, and each is cheap next to what it replaces. The aim was never to own everything. And Move 03 gives you permission to stop: if the arithmetic does not clear a third, three Moves and a week is the whole cost of finding out.

Rehearse everything, and read the Rollback before the first step of every Move — including the ones that look like nothing.

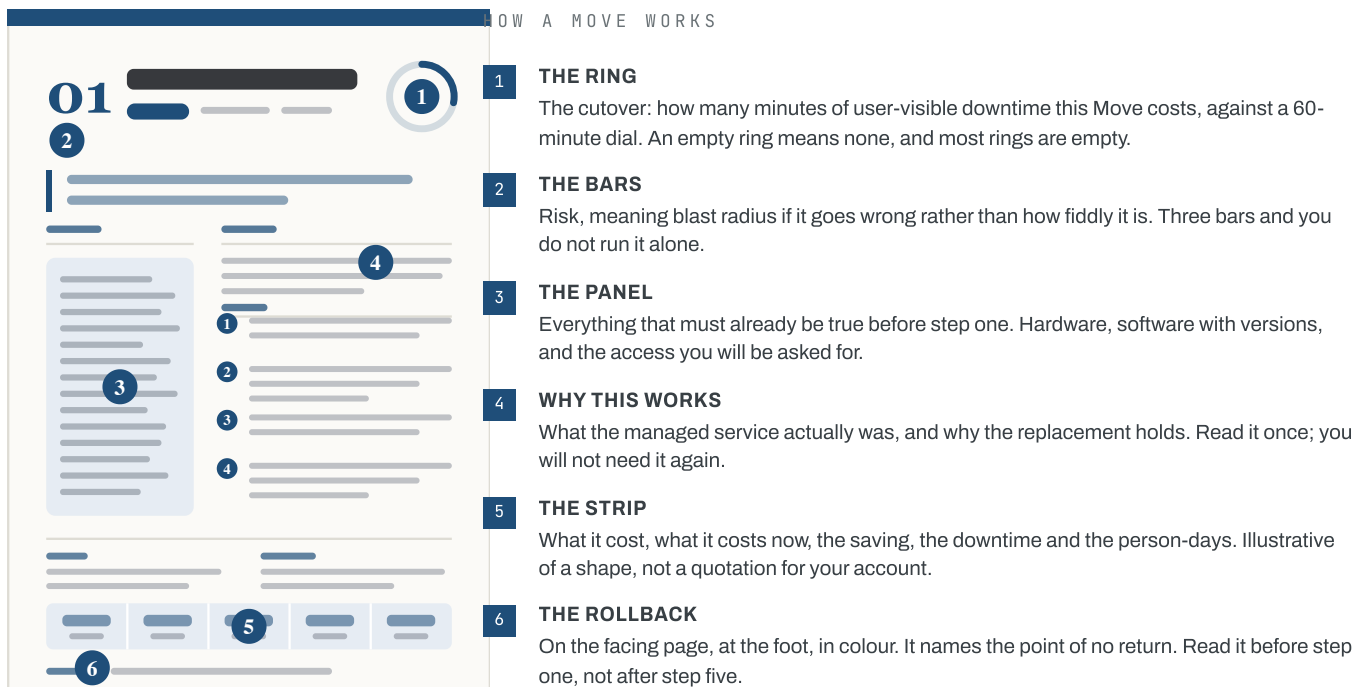

EVERY MOVE, WITHOUT EXCEPTION

WHY LEAVE AT ALL

A cloud bill is rent on somebody else's margin, charged by the byte, for as long as you exist. On the estate this book is written against it comes to \$1,007,973 over the life of one generation of machines — which is two engineers, or a year of

runway, or the difference between raising again and not. That is the whole argument. Everything below is either a way of checking it or a reason it might not apply to you.

WE DID THIS, AND HERE IS WHAT ACTUALLY HAPPENED

730 days

at 99.993 per cent measured availability, through a period that included a region-wide outage at the cloud we had left

19%

lower latency on the same software, from local NVMe and the absence of neighbours. We bought no faster code to get it

2

hardware interventions in twenty-four months, both disks, both handled by remote hands with a mean response of twenty-seven minutes

0

people hired. The toil moved; it did not multiply. We measured it at about fourteen engineer-hours a month across two sites

Our own fleet and our own measurement, not an independent audit, and a bigger estate than this book is sized for. The rest of the figures here stand on outside sources and on arithmetic you can repeat.

1 THE BILL STOPS BEING A PERCENTAGE OF YOUR GROWTH

This is the one that matters and the rest are consequences of it. A cloud bill is a toll on activity: more users, more bytes, more bill, for ever, at a margin somebody else sets and can change. A rack is a fixed cost. It costs the same in the month you double as in the month you do not, and the only thing that grows is the power draw, by the watt rather than by the invoice line. Over five years the difference here is \$1,007,973, and the machines are still working at the end of it.

CHECK IT

Take last quarter's invoices and plot the total against your own usage metric. If the line is flat you have nothing to gain here. If it tracks your growth, that slope is what you are buying out of — Move 01.

2 EGRESS STOPS BEING A TAX ON YOUR OWN TRAFFIC

Moving your own data to your own users is where the margin lives, and it is the line that ends most of these arguments: \$7,980 a month to send a hundred terabytes out. Transit at a facility is bought by the megabit and costs a small fraction of that. Nothing you build gets faster and no code changes; the line simply stops being there.

CHECK IT

Find the data-transfer line on last month's bill. Divide it by your egress in terabytes. If it is anywhere near ninety dollars a terabyte, that line is nearly pure margin — Move 01, then Move 18.

3 THE MACHINES ARE YOURS, SO THE PERFORMANCE IS YOURS

A vCPU is half a core somebody else is also using. Local NVMe is not a network service with a queue in front of it and a token bucket on top. The gain is not theoretical and it is not small: on identical software we measured nineteen per cent, and the noisy-neighbour tail — the ninety-ninth percentile that wakes people — improves more than the mean does.

CHECK IT

Compare your ninety-ninth percentile against your median for a week. If the gap is wide and unexplained by your own code, some of it is not yours — Move 14 measures it on real hardware before anything moves.

4 NOBODY DEPRECATES YOUR HARDWARE

A managed service is somebody else's roadmap running inside your product. Instance families are retired, versions go end-of-life on a date you did not pick, a control plane upgrades on its own release channel, and the longest you can hold it is ninety days. A machine you own runs the version you chose until you choose another one, and the migration happens when you have time rather than when the notice arrives.

CHECK IT

Count the forced upgrades and deprecation notices you have absorbed in the last two years, and what each cost in engineer-days. That is a recurring bill nobody invoices you for.

5 YOU CAN BE TOLD NO, AND IT STOPS MATTERING

Capacity in your region, a quota nobody will raise, a region-wide outage you can do nothing about except write a status update. Owning hardware does not make you immune to failure — it makes the failure yours to fix, at three in the morning, without a support tier and without waiting. Whether that reads as a gain or a cost depends entirely on whether you would rather be working or waiting, and you already know which you are.

CHECK IT

Look up the last provider incident that hurt you. Ask what you could have done differently with root on the machines. If the answer is nothing, this one is worth real money to you.

AND WHAT IT COSTS YOU

All of that is real and none of it is free. Four things get worse, and a comparison that leaves them out is

the reason repatriations get approved and then regretted.

1 CAPITAL, ON DAY ONE

About \$87,000 leaves the bank before anything serves a request. On eighteen months of runway that is a fair refusal, and Move 07 tells you what to do instead.

2 LEAD TIME YOU CANNOT COMPRESS

Hardware is ordered, not provisioned. A cage is signed, a circuit is delivered, and the calendar for this programme is mostly waiting: of the 32 weeks end to end, only 80 days are anybody working.

3 THE PAGER, AND ABOUT 20 MORE HOURS A MONTH

Somebody carries it, and it is now a machine rather than a ticket. We measured our own two-site fleet, which is larger than the one this book is written against, at fourteen engineer-hours a month; the book books 80 against the 60 the cloud estate was already taking, because we had done it once before and you will not have.

4 THREE THINGS THAT NEVER COME HOME

A content delivery network, outbound mail deliverability and scrubbing at the edge are businesses other people run better than you will. Move 04 tells you to keep paying for all three, and they are \$2,310 a month of the after state for ever.

WHEN TO STAY EXACTLY WHERE YOU ARE

Your load is spiky or seasonal and genuinely scales to near nothing between the spikes. Elasticity is the one thing a rack cannot do, and paying for the peak all month is how owning becomes the expensive answer.

Nobody on the team wants to run infrastructure. This is a trade, not a free lunch, and it is paid for in attention. A team that resents the pager will run the platform badly and blame the hardware.

You lean hard on managed services that have no real equivalent - a serverless database, a hosted stream, a workflow engine - and replacing them is a rewrite rather than a migration. Move 02 will tell you this in an afternoon.

The bill is small. Below about ten thousand dollars a month the saving is real and the distraction is larger; Move 03 gives you permission to do the arithmetic and stop, and stopping is a perfectly good outcome.

If none of those four is true and the arithmetic in Move 03 clears, the rest of this book is twenty jobs that get you there, each one done on a Tuesday and undone on a Wednesday.

THE REFERENCE BUILD

Every Move in this book is written against one cluster, so that a runbook can name a real thing rather than a category: one site, 5 nodes and 1 on the shelf, 32 cores and 256 GB a node, 25 GbE to the switch. 5 because three is the smallest control plane with a quorum and losing one of three leaves two machines carrying a load nobody sized them for; the spare because a dead board is a return authorisation and three weeks. Scale the numbers; do not scale away the redundancy.

COMPUTE

- ☐ Five 1U dual-socket servers, and a sixth on the shelf
- ☐ 32 physical cores a node, current-generation EPYC or Xeon
- ☐ 256 GB ECC memory a node, all channels populated
- ☐ Redundant hot-swap power supplies, each fed from a different strip
- ☐ A management controller on every node - Redfish, not just a web console

STORAGE

- ☐ Four NVMe drives a node, mixed-use endurance, 3.84 TB each
- ☐ Enterprise drives with power-loss protection - not consumer SSDs
- ☐ A separate boot pair, mirrored
- ☐ One spare drive of each size, on site, unopened
- ☐ A backup target at a provider you are not otherwise using

NETWORK AND SPACE

- ☐ Two 25 GbE switches, stacked or in a link-aggregation pair
- ☐ Two uplinks a node, one to each switch
- ☐ A separate 1 GbE management switch, not reachable from the internet
- ☐ A quarter rack in a carrier-neutral facility, A and B power
- ☐ Facility transit for go-live, and a second upstream ordered alongside it
- ☐ An out-of-band line that works when the main path does not

THE SOFTWARE STACK

- ☐ Talos Linux on every node - no shell, no package manager, no drift
- ☐ Kubernetes, on a version at least one minor behind the newest
- ☐ Cilium for the cluster network, with kube-proxy replaced
- ☐ Rook, and the Ceph cluster it manages
- ☐ CloudNativePG, on local NVMe rather than on Ceph
- ☐ cert-manager and Envoy Gateway
- ☐ Argo CD, with the cluster state in Git
- ☐ Prometheus and Loki for the stores, OneUptime for what wakes somebody
- ☐ Velero, and a restore you have actually performed

ACCESS

- ☐ An identity provider that is not the cluster
- ☐ Break-glass credentials in a safe, on paper
- ☐ A jump host or a mesh - never a public API server
- ☐ Hardware tokens for anyone who can delete a cluster
- ☐ A status page that is not hosted on the thing it reports on
- ☐ The domain registrar account locked, with recovery codes printed

ON THE LAPTOP

- ☐ kubectl
- ☐ helm
- ☐ talosctl
- ☐ k9s
- ☐ argocd
- ☐ velero
- ☐ psql and pg_dump
- ☐ barman-cloud
- ☐ redis-cli
- ☐ rclone
- ☐ the cloud CLI, still logged in
- ☐ dig and mtr
- ☐ openssl
- ☐ ipmitool
- ☐ the runbook, printed

THE ON-RAMP

Almost nobody should sign a facility contract before they have run this stack once. A cluster of 3 refurbished machines with 12 cores and 64 GB each, on a managed switch under a desk, will run every Move in Stage 3 unchanged and most of Stage 4 besides. It costs about \$3,430 once and about \$30 a month in electricity, it saves nothing whatsoever, and it is the cheapest way to find out whether the rest of this book is for you.

WHY THREE, AND WHY SECOND-HAND

Three because a control plane needs three members to lose one and keep going, and everything you will learn about quorum, fencing and upgrades needs somewhere to go wrong. Second-hand because a machine two generations old runs Kubernetes exactly as well as a new one at roughly a tenth of the price, and because you want to be willing to break it.

WHAT IT CANNOT TEACH YOU

Every word of Stage 2. A homelab has one power feed, one switch, no cross-connect, no remote hands and nobody to escalate to at three in the morning. It cannot show you what a colocation contract is for, or what happens when the A feed goes away and the B feed was never tested. The building is a different discipline, which is why it has a stage of its own.

THE ONE PART TO BUY NEW

The drives. A consumer SSD without power-loss protection will corrupt etcd the first time the power flickers, and it will do it in a way that looks like a Kubernetes bug for a day and a half. Buy small enterprise NVMe with the protection, second-hand if you like, and put the money you saved on the chassis into the disks.

WHAT IT GENUINELY PROVES

The whole software estate. Talos, the control plane, Cilium with kube-proxy replaced, Rook and Ceph, the registry, secrets, the observability stack, and a Postgres cutover rehearsed end to end against a copy. If a Move works here it will work on the metal; the difference is scale, not shape.

WHEN TO STOP USING IT

Never. The on-ramp becomes the non-production cluster the rest of the book keeps asking for — the one you restore etcd onto, rehearse an upgrade on, and point a load generator at. Every estate needs a cluster it is allowed to destroy, and this is the cheapest one you will ever own.

IF THREE MACHINES AT HOME IS NOT POSSIBLE

Rent three of the cheapest dedicated hosts you can find, by the month, and run exactly the same experiment. It costs more than electricity and less than being wrong, it gives you real addresses and a real network, and you can hand it all back at the end of the month. What it will not give you is a machine you can physically pull a disk out of.

THE WHOLE SHOPPING LIST

- ☐ Three refurbished mini PCs or small-form-factor desktops
- ☐ 64 GB in each - memory is what runs out first, not cores
- ☐ Two NVMe drives a node: one to boot, one for data
- ☐ A managed switch with VLANs and a spare port for out-of-band
- ☐ A small uninterruptible power supply, mostly to survive the brownouts that corrupt etcd
- ☐ A domain you own, for real certificates rather than self-signed ones

THE RULES FOR LEAVING THE CLOUD

- **1 Move the cheapest thing first.** Not the most expensive. The first Move exists to prove the platform and the team, and it should be something whose failure is a shrug. You are buying evidence, and evidence is worth more early than savings are.
- **2 Data moves last and leaves last.** Every stateless thing can be cut over and cut back in minutes. State cannot. Move compute first, run it against the cloud database across the link, and only then move the database - by which point you have already learned the things you would otherwise learn during a data migration.
- **3 Never run two platforms longer than you planned to.** The cost of leaving is not the hardware. It is the months in which both estates are live, both are on call, and every change has to be made twice. Pick the overlap window before you start, write it down, and treat overrunning it as the incident it is.
- **4 Keep the bill until the invoice proves you can stop.** A resource is not decommissioned when nothing points at it. It is decommissioned when a full month has passed, the line has gone from the bill, and nobody has filed a ticket. Turning things off too early is how a migration becomes an outage a fortnight later.
- **5 Buy the second of everything, and one spare.** Two switches, two power feeds, two people who can get into the building, and a sixth machine that is already burned in. Every single point of failure you accept at the start becomes an incident you attend in person, at night, in a year.
- **6 Count the salary.** A saving that costs engineer-hours is a real saving only if you write the hours into the comparison - on both sides, because the cloud takes them too. Most of these still win by a wide margin once you do. The ones that do not, you want to know about in week one rather than month ten.
- **7 Keep paying for the three things you will not beat.** A content delivery network, denial-of-service scrubbing at the edge, and outbound email deliverability. Each is a business somebody else already runs better than you will, and each is cheap next to what it replaces. Ownership is a means, not a principle.

BEFORE YOU TOUCH ANYTHING

Every Move in this book changes something that is running. Most are reversible for a stated window, a few only until a particular step, and none of them is irreversible, which is a property of this edition rather than of the work: every Move here was chosen so that it could be undone. The difference between a migration and an incident is almost never the technique - it is whether somebody worked out the way back before they started, and whether anybody had ever tested it.

READ THE ROLLBACK FIRST

Not the runbook. The Rollback section of every Move names the point of no return: the step after which the old system can no longer serve traffic or no longer holds current data. Read it, decide whether you are willing to reach that step today, and only then start at step one.

KEEP THE OLD THING RUNNING, AND KEEP PAYING FOR IT

The instinct after a successful cutover is to delete the source and book the saving. Do not. The Reversible field on each Move is how long the old system must stay warm, powered and receiving its own backups. That overlap is the entire cost of being wrong, and it is cheap.

WRITE DOWN THE STATE YOU CANNOT RECREATE

Before Stage 4, list every store whose contents exist nowhere else: the primary database, the uploads bucket, the secrets, the certificate private keys, the recovery codes for the accounts that own the domain. Everything else is rebuildable from a repository. That list is short, and it is the only part of the estate where a mistake is permanent.

TWO PEOPLE, ONE KEYBOARD

Every High-risk Move in this book assumes a second person who is not typing, is reading the runbook aloud, and has the authority to stop. It is the cheapest safety control in infrastructure and the first one teams drop when they are behind schedule. With two engineers on the whole programme, it is also the one you are most tempted to skip.

A BACKUP NOBODY RESTORED IS NOT A BACKUP

It is a file. Before Stage 4, restore the backup you are relying on into a scratch environment and count the rows against production. The number of companies that discover their backups were empty during the incident that needed them is not small, and every one of them had a green dashboard.

CUT OVER WHEN YOU CAN UNDO IT, NOT WHEN YOU ARE CONFIDENT

Confidence is not evidence. The right time to move traffic is when the rollback has been rehearsed end to end, on the same day of the week, with the same people awake. A Tuesday morning with the team at their desks beats a Saturday night with one person and a laptop, every time.

VERIFY BY COUNTING, NOT BY LOOKING

A migration is finished when the destination answers the same questions as the source with the same answers. Row counts, checksums, a replayed hour of real traffic compared response by response. A page that loads is not evidence, and neither is an application that starts.

STOP WHEN YOU ARE SURPRISED

Not when something breaks - when something is merely unexpected. A row count that is off by eleven, a certificate with the wrong issuer, a replica that caught up faster than it should have. Surprise means the model in your head and the system in front of you have diverged, and continuing is guessing.

These are operational practices, not a warranty. The runbooks in this book were written against the services and versions named in each Move and will drift as those change. Rehearse every Move against a copy of your own estate before you run it against the real one, and treat any figure here as the shape of an answer rather than a quotation for your account.

WHAT IT ACTUALLY COSTS

The comparison that gets a repatriation approved and then regretted is the one that counts the hardware and forgets the people. This one counts both, at list price and with no commitment discount on either side, for the reference build opposite. Substitute your own effective rate; the shape does not change.

ON AWS, COMPUTE ALONE

320 vCPU of current-generation general purpose instances, on demand, is **\$11,773** a month before a single gigabyte of storage, a load balancer or a byte of egress. Egress is the line that ends most arguments: 100 TB a month is \$7,980, every month, for the privilege of your own traffic leaving.

RENTED BY THE MONTH

The same class of machine from a dedicated-host provider is \$3,900 — MORE than owning, not less, and it should be: over 60 months you hand over \$234,000 for machines that cost \$78,000 to buy, which is 3.0 times the purchase price. A landlord buys the same box you would and takes a margin. What renting actually buys is no capital, no lead time, no cage and no contract, and it lands within a few hundred dollars a month of owning because it drops the facility. On eighteen months of runway that is the right trade; it is not a cheaper one.


OWNED, IN ONE QUARTER RACK

\$3,235 of infrastructure - metal amortised over five years, the spare, power, the space, transit, the cross-connect and remote hands - plus \$1,830 of additional salaried time and \$2,310 that never comes home at all: the edge, the outbound mail and the scrubbing of Move 04, and the residue five later Moves leave behind. That salary line is the largest number in this column, the retained line is the one every other comparison forgets, and a table without either is the reason repatriations get approved and then regretted. Total **\$7,375** a month.

WHAT THE DIFFERENCE BUYS

\$16,625 a month, or \$199,500 a year, for a capital outlay of \$87,000 — six machines and a pair of switches — which pays for itself in about 5 months. That is 56 per cent of a fully loaded \$29,491, with the salary counted on both sides; on the infrastructure line alone, which is what every other comparison quotes, it is 77 per cent. Both are true and the difference between them is the people.

ONE ESTATE, THREE WAYS, PER MONTH

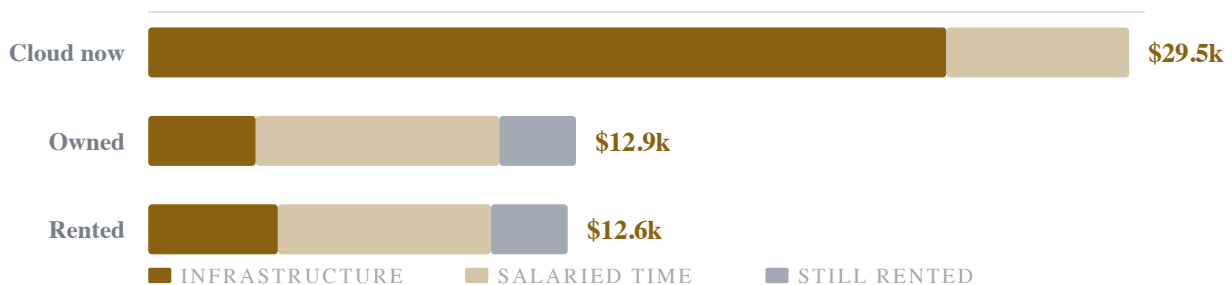

Every AWS figure is a public list price for us-east-1 observed while writing, before any Savings Plan, private pricing agreement or credit. Every hardware figure is a mid-market street price for the specification opposite. Both will drift. The comparison is a method you can repeat against your own invoice, not a quotation - and if your effective rate is half of list, halve the left-hand column and read the conclusion again.

FIVE YEARS, THREE WAYS

A month is the wrong window for a capital decision. Owning is capital on day one and cheap running afterwards; renting is no capital and dearer running; the cloud is no capital and dearest running. Compared a month at a time the capital either vanishes into an amortisation line or sits there looking like the whole story, and neither is what somebody signing the cheque is choosing between.

THE SAME COMPUTERS, THREE WAYS, OVER 5 YEARS

	CAPITAL	RUNNING, A MONTH	TOTAL OVER 5 YEARS	AGAINST THE CLOUD
Cloud	–	\$29,491	\$1,769,480	–
Rented metal	–	\$12,617	\$756,993	\$1,012,487 (57%)
Colocation	\$87,000	\$11,459	\$761,506	\$1,007,973 (57%)

Over five years the two metal columns land within \$4,513 of each other, and the whole of that difference is the residual: machines of this class run seven or eight years, so after sixty months you still hold a working fleet, counted here at a conservative fifteen per cent of what it cost. You do not own hardware to beat renting it. You own it when the fleet is big enough to carry the room.

WHAT REPLACES WHAT

Every Move names the real service on all three clouds and the one thing that differs on each, so this table is the map rather than the content. Find the row you are paying for and then read the Move. The right-hand column is the point of the whole book, and where it says keep paying, that is a conclusion rather than a gap.

AWS	GOOGLE CLOUD	AZURE	WHAT YOU RUN INSTEAD
EC2	Compute Engine	Virtual Machines	Bare metal you own, or dedicated machines by the month
EC2 Auto Scaling	Managed instance groups	Virtual Machine Scale Sets	Fixed capacity, a priority class, and a spare on the shelf
EKS	GKE	AKS	Talos Linux, and Kubernetes you run yourself
ECS on Fargate	Cloud Run	Container Apps	Deployments and Jobs on your own nodes
AMI	Machine images	Managed images	A Talos machine configuration, applied over the network
VPC	VPC networks	Virtual Network	Two switches, four ranges, and an address plan on one page
EBS	Persistent Disk	Managed Disks	Ceph RBD under Rook, with local NVMe underneath it
EFS	Filestore	Azure Files	CephFS under Rook, or a filesystem the application stops needing
S3	Cloud Storage	Blob Storage	Ceph's S3 gateway - deep archive stays where it is
RDS for PostgreSQL	Cloud SQL for PostgreSQL	Database for PostgreSQL	PostgreSQL under CloudNativePG, on local NVMe
ElastiCache	Memorystore	Azure Cache for Redis	Valkey for the half that is really a cache
SQS and SNS	Pub/Sub	Service Bus	NATS JetStream, or a table in the database you already have
Glacier Deep Archive	Archive storage class	Archive tier	Keep paying - the egress to extract it costs more than the years
AWS Backup	Backup and DR Service	Azure Backup	Velero and the database operator's own archive, held somewhere else
Application Load Balancer	Cloud Load Balancing	Application Gateway	Envoy Gateway behind a virtual IP that fails over

WHAT REPLACES WHAT II

The rows that say keep paying are set in red because they are the most important lines in the table. A content delivery network, scrubbing capacity at the edge and outbound mail deliverability are not technical problems you have not solved yet. They are businesses, and you are not in them.

AWS	GOOGLE CLOUD	AZURE	WHAT YOU RUN INSTEAD
ACM	Certificate Manager	Key Vault certificates	cert-manager, issuing and renewing without anybody watching
Route 53	Cloud DNS	Azure DNS	Two independent authoritative providers, never one
NAT Gateway	Cloud NAT	NAT Gateway	Node addresses, and one translation hop for the few that need it
CloudFront	Cloud CDN	Azure Front Door	Keep paying - change vendor, not model
AWS Shield and WAF	Cloud Armor	Azure DDoS Protection and WAF	Keep paying for scrubbing - the capacity is upstream of you
SES	No first-party equivalent	Communication Services	Keep paying for outbound - inbound can come home
ECR	Artifact Registry	Container Registry	A pull-through cache, then your own registry of record
Secrets Manager	Secret Manager	Key Vault	Encrypted in the repository, with the key held outside the cluster
CodeBuild	Cloud Build	Azure Pipelines	Runners on the machines you already own and are not using
CloudWatch metrics	Cloud Monitoring	Azure Monitor	Prometheus, with a cardinality budget agreed in advance
CloudWatch Logs	Cloud Logging	Log Analytics	Loki, sized against retention somebody actually chose
CloudWatch alarms	Cloud Monitoring alerting	Azure Monitor alerts	OneUptime - alerting, on-call rotas, incidents and a status page
Cost Explorer	Cloud Billing reports	Cost Management	A model built from invoices, counting power, spares and the rota
Organizations	Organisation and projects	Subscriptions and Entra	One account left open only until the last invoice reads zero

WORK OUT WHETHER TO DO IT AT ALL

DONE WHEN You know what you spend, what you would spend instead, and whether it is worth it.

Whether to do this at all. Three Moves of arithmetic against your own invoice, and a fourth that names what stays rented. The stage most likely to end the programme, and that is a success rather than a failure.

☐	01	The bill, and the three lines that are most of it	0 min	24
☐	02	What you actually run	0 min	26

☐	03	The number that decides it	0 min	28
☐	04	The three things you keep renting	0 min	30

ORDER THE HARDWARE AND SIGN THE SPACE

DONE WHEN The machines are on order and the cage is signed.

What to order and where to put it. Nothing here is software, and getting it wrong is the only mistake in this book you cannot fix with a deploy. Both clocks start in this stage, and they run in parallel.

☐	05	From rented vCPUs to cores you own	0 min	34	☐	07	A cage, not a data centre	0 min	38
☐	06	Five machines, and the one on the shelf	0 min	36	☐	08	The order, and the weeks you cannot compress	0 min	40

TURN THE BOXES INTO A CLUSTER

DONE WHEN A cluster that could take production traffic, and never has.

Everything between a racked machine and a cluster that could take production traffic. Nothing here moves a workload; all of it decides how well the rest of the book goes.

☐	09	Racking day	0 min	44	☐	11	A cluster, in an afternoon	0 min	48
☐	10	The network, and the way back in when it breaks	0 min	46	☐	12	Disks: what goes local, what goes on Ceph	0 min	50

MOVE THE APP, THEN THE DATA

DONE WHEN Everything runs on your machines, and the cloud copy is still warm.

The application first, then the state. The stage that can lose a company its data, and therefore the one with the longest overlap windows, the most rehearsal and the fewest one-way steps.

☐	13	Images, secrets and one-command deploys	0 min	54	☐	15	Buckets, cache and queues	0 min	58
☐	14	The first service, end to end	0 min	56	☐	16	Postgres, the one that matters	15 min	60

CUT THE TRAFFIC OVER, AND KEEP IT ALIVE

DONE WHEN Users reach your machines, you can carry it at 03:00, and the cloud bill is zero.

The traffic, the pager and the last account. Every article about leaving the cloud stops before this stage, and every migration that regrets itself failed inside it.

☐	17	The front door	0 min	64
☐	18	Go-live, and how you abort	10 min	66
☐	19	Backups you have restored, and the pager	0 min	68
☐	20	Closing the account	0 min	70

DECIDE

The invoice, the inventory and the comparison with the salary line in it. Three Moves, about a week, and permission to stop.

BUY

The specification, the machines, the space and everything with a lead time. The stage where a mistake costs a lorry rather than a deploy.

BUILD

Racking, the network, the cluster and the disks. Nothing here moves a workload, and everything here decides how the rest goes.

MOVE

Images and secrets, the first service, the buckets and the database. The longest overlaps and the most rehearsal in the book.

RUN

The edge, the cutover, the backups you have restored, the pager, and the account you finally close.

Every Move states its cutover in minutes of user-visible downtime, its risk as blast radius rather than difficulty, and how long the thing it replaced must stay warm before you turn it off. 18 of the 20 Moves in this book cost no downtime at all; the whole book, executed end to end, costs 25 minutes.

WHICH MOVE DO I NEED

Nobody opens a book like this at Move 01. They open it because something on the bill, or on the pager, has become intolerable. This is the index for the way the question actually arrives.

The bill went up and nobody can say why

- 01 The bill, and the three lines that are most of it
 02 What you actually run 03 The number that decides it
-

Egress is now one of the largest lines on the invoice

- 01 The bill, and the three lines that are most of it
 14 The first service, end to end 18 Go-live, and how you abort
-

We have no idea what we are actually running

- 02 What you actually run
 13 Images, secrets and one-command deploys 20 Closing the account
-

The hardware sounds like a full-time job nobody has

- 07 A cage, not a data centre 09 Racking day
 11 A cluster, in an afternoon
-

Nobody wants to be on call for a machine

- 09 Racking day 19 Backups you have restored, and the pager
 06 Five machines, and the one on the shelf
-

Somebody has asked what would happen if we just left

- 03 The number that decides it 04 The three things you keep renting
 07 A cage, not a data centre
-

The database costs more than the engineers who query it

- 05 From rented vCPUs to cores you own
 12 Disks: what goes local, what goes on Ceph
 16 Postgres, the one that matters
-

We are being asked to do this and we have two engineers

- 03 The number that decides it
 06 Five machines, and the one on the shelf
 19 Backups you have restored, and the pager
-

Something has to move this quarter and nothing may break

- 14 The first service, end to end 17 The front door
 18 Go-live, and how you abort
-

We were told we cannot leave, and nobody has checked

- 04 The three things you keep renting 15 Buckets, cache and queues
 20 Closing the account
-

I DECIDE

Whether to do this at all. Three Moves of arithmetic against your own invoice, and a fourth that names what stays rented. The stage most likely to end the programme, and that is a success rather than a failure.

4 MOVES	4 ZERO DOWNTIME	0 HIGH RISK	0 MINUTES, TOTAL
------------	--------------------	----------------	---------------------

IF YOU ONLY DO THREE

01

THE BILL, AND THE THREE LINES THAT ARE MOST OF IT

The invoice records what you were charged, not what you use. Read it to the line, find the three that are most of it …

04

THE THREE THINGS YOU KEEP RENTING

Three capabilities do not come home: the edge, outbound mail and volumetric scrubbing. Naming them now keeps the plan …

02

WHAT YOU ACTUALLY RUN

The estate feels infinite because nobody has written it down. On one page it is forty rows, and every row has a name …

THE BILL, AND THE THREE LINES THAT ARE MOST OF IT · WHAT YOU ACTUALLY RUN · THE NUMBER THAT DECIDES IT · THE THREE THINGS YOU KEEP RENTING

■ 3 LOW RISK

■ 1 MEDIUM RISK

01 THE BILL, AND THE THREE LINES THAT ARE MOST OF IT

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
DECIDE	—	LOW	IMMEDIATELY

The invoice records what you were charged, not what you use. Read it to the line, find the three that are most of it, then start the clock on working set.

AWS	Cost Explorer	hourly and resource-level granularity is a paid opt-in, and that detail is then kept for 14 days.
GOOGLE	Cloud Billing reports	detailed usage cost reaches BigQuery only from the day the export is enabled, and is never backfilled.
AZURE	Cost Management	amortised reservation cost appears on an Enterprise Agreement account, not on pay-as-you-go, and exports land in Blob Storage on a schedule.

BEFORE YOU START

ACCESS

- Billing owner rights in every cloud account, and permission to install an agent on production instances

SOFTWARE

- The provider tools aws, gcCloud and az, none older than six months
- A spreadsheet and a time-series store with three weeks of retention

PEOPLE

- Whoever signs the invoice, for half an hour at the end

WHY THIS WORKS

Three numbers decide everything that follows, and none is on the provider's default dashboard. A bill records what was charged — allocation, commitment, a support percentage — not what the machines were doing. Grouped into compute, state and traffic, two hundred line items collapse into three piles, and three lines usually carry eighty per cent of the spend. The window runs alongside, because the figure a purchase order needs is working set and the hypervisor cannot see it. Two weeks, not thirty days: this is a five-machine decision, and more precision would not change the order.

SWAP

If finance already breaks the bill down by service, start there and spend the saved day on step four. The categories will be wrong, the totals right.

DO IT FASTER

Pull three invoices rather than one. One month hides a reservation renewal and a support tier that stepped up.

WATCH OUT

Agent metrics are billed differently on each cloud — per unique metric a month on one, per sample ingested on the others — and an agent collecting every counter it finds has produced four-figure surprises on all three. Name the metrics you want.

LEFTOVERS

The agents, export jobs and extra ingestion bill on until somebody removes them. Diary it for the day the hardware order is signed.

—	—	—	0 min	3 days	2 weeks
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing, yet. This Move moves one line upward: a fortnight of custom metrics, the cheapest few hundred dollars in the programme.

- 01 Export one month at line-item granularity from every account, not the summary view. That means the detailed export rather than the console API on all three: the Cost and Usage Report delivered to a bucket, a BigQuery billing export, and `az costmanagement export` per subscription. `aws ce get-cost-and-usage` and the reports page return period totals grouped two ways at most, which is the summary view under another name.
- 02 Put every line in the spreadsheet, one row each, tagged compute, state or traffic: instances and containers; managed databases, caches and object storage; egress, balancers and the CDN.
- 03 Sort by amount and rule a line under the third row. Those three are the programme; anything beneath worth under two per cent of the invoice is not discussed again.
- 04 Reconcile the export against what you believe you run. Enumerate the accounts first — `aws organizations list-accounts`, `gcloud billing projects list` against each billing account, `az account list` — because the forgotten estate is usually in an account nobody named. Lines nobody owns are idle balancers, volumes of dead instances, a staging project that shipped. Expect five to fifteen per cent.
- 05 Install the memory agent where it is missing and point one time-series store at all three metric APIs. No hypervisor sees inside its guests, so working set arrives only from within the machine.
- 06 Open the window for a fortnight, and record what resists measurement: burstable credits, page cache against anonymous memory, build minutes that were never an instance.

ROLLBACK

Nothing in production changes, so backing out is removing an agent and stopping an export job. There is no point of no return here; the first is the hardware order, signed against these numbers. A sampling window cannot be rerun retrospectively, so stopping at day nine means starting over. If the time-series store is lost, restore it.



02 WHAT YOU ACTUALLY RUN

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
DECIDE	—	LOW	IMMEDIATELY

The estate feels infinite because nobody has written it down. On one page it is forty rows, and every row has a name against it.

AWS	Resource Explorer	indexes per Region behind one aggregator and searches one account until the organisation-wide view is on, so the second account stays invisible.
GOOGLE	Cloud Asset Inventory	the caller needs <code>cloudasset.assets.searchAllResources</code> at the organisation scope; a project-level grant says nothing about the siblings on the same invoice.
AZURE	Resource Graph	reads only subscriptions the caller can already see, and pages at 1,000 rows, so an unpaginated query returns a truncated estate that looks complete.

BEFORE YOU START

ACCESS

- Read-only access to every cloud account, project and subscription, including the forgotten ones
- The billing export from Move 01, at resource granularity rather than by service

SOFTWARE

- The provider's asset CLI — `aws`, `gcloud` or `az` — and one shared document with a row per resource

PEOPLE

- The engineer who would notice each service stopping, named on every row

WHY THIS WORKS

Leaving the cloud feels impossible because nobody can say what would have to move. The estate lives in three or four heads, so the total is always imagined larger than it is. A company spending \$24,000 a month usually runs a dozen services, one Postgres, one cache, two or three buckets and a handful of scheduled jobs. That fits on a page, and every later Move then has something finite to count against. Nothing changes here: this Move reads, and writes down what it read. The risk is being wrong about what runs, and the bill settles that.

SWAP

Where accounts are few and tags honest, the provider's tag report is a quicker first pass. Untagged resources still have to be found by hand.

DO IT FASTER

Reconcile before assigning owners. The bill sorts rows by cost, which is the order worth arguing about.

WATCH OUT

These inventories list what the provider created. What a third party stood up against your account — an agent, a contractor's sandbox — appears nowhere else.

LEFTOVERS

A snapshot outlives the volume it came from and bills long after the rest of its account has gone. So does a retained log group.

—	—	—	0 min	3 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF The fourth pile, once its owners confirm: orphaned volumes, snapshots of vanished disks, idle load balancers and the proof-of-concept accounts. The cheapest saving in the book.

NEEDS 01 The bill, and the three lines that are most of it

THE RUNBOOK

- 01 Pull the machine-readable list, one account at a time: `aws resource-explorer-2 search, gcloud asset search-all-resources` or `az graph query`. Paste it into one document, a row per resource.
- 02 Add what those APIs never return: scheduled jobs, queues, third-party services with a webhook into production, and the DNS records pointing at any of it.
- 03 Reconcile against the billing export from Move 01 both ways. A bill line with no row is unowned; a row with no bill line is free, or in an account nobody has opened.
- 04 Hunt what hides: snapshots whose disk is gone, volumes attached to nothing, load balancers with no target, staging at full size overnight, the accounts opened for a proof of concept in 2022.
- 05 Sort every row into one of four piles — moves as-is, moves with work, stays rented, gets deleted. The fourth is the biggest; confirm each row with its owner and check thirty days of metrics first.

ROLLBACK

Nothing here touches a running system, so backing out is discarding a document nobody acted on. The point of no return is the fourth pile: once a resource on it is deleted, getting it back means a restore from whatever snapshot survives, and for a log group there may be none. Keep the inventory in version control.



DECIDE • 0 MIN • LOW RISK

The fourth pile, once its owners confirm: orphaned volumes, snapshots of vanished disks, idle load balancers and the proof-of-concept accounts. The cheapest saving in the book.

03 THE NUMBER THAT DECIDES IT

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
DECIDE	—	MEDIUM	IMMEDIATELY

Two columns, five years of amortisation and one salary line. If owned is not a third under rented, the answer is to stop, and stopping here is cheap.

AWS	AWS Pricing Calculator	two tools now carry that name, and only the one inside the billing console can see the Savings Plans your account already holds.
GOOGLE	Google Cloud Pricing Calculator	the only discount it models is a committed-use one you pick from a dropdown, and its default machine series earns no sustained-use discount at all.
AZURE	Azure Pricing Calculator	signing in and selecting the Enterprise Agreement licensing programme rewrites every price on the page, so an anonymous quote is retail and not yours.

BEFORE YOU START

ACCESS

- Three recent invoices at the rate you actually paid, not list
- A written quote for the five machines and one for a quarter rack

SOFTWARE

- One spreadsheet, two columns: owned on the left, rented on the right

PEOPLE

- Whoever carries the pager, because the salary line here is theirs

WHY THIS WORKS

Moves 01 and 02 produced a grouped bill and an inventory that accounts for it. This Move sets the two candidate estates beside each other. The arithmetic is not hard; the discipline is refusing to leave anything out of the owned column, because an omitted line is what somebody finds in month five with two platforms running. The rule goes in before the numbers, so they cannot be argued into the answer somebody wanted. Nothing has been bought and no traffic has moved; two days of somebody's time is the whole exposure.

SWAP

Price the three largest lines only; that lands within about ten per cent in an afternoon.

DO IT FASTER

Use one calculator, not three. The comparison is owned against what you pay now, not a cheaper landlord.

WATCH OUT

The ops-hours line moves the answer further than anything else in the sheet, and it is the one people guess at. Amortisation over seven years instead of five shifts the total by about three per cent; doubling the hours you think owning will take shifts it by ten times that. Put your own number in before you argue with the conclusion.

LEFTOVERS

The committed-spend agreement bills to the end of its term, and that renewal date is the deadline.

—	—	—	0 min	2 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing yet. This Move produces a number and, with it, permission to act or to stop.

NEEDS 01 The bill, and the three lines that are most of it 02 What you actually run

THE RUNBOOK

- 01 Write the decision rule before any figure goes in: owned must land at least a third under rented, or the programme stops here. A thinner margin sits inside your own forecasting error.
- 02 Fill the rented column from the three invoices at the rate you actually paid, discounts in and tax out on both sides. One monthly number, checkable against Move 01.
- 03 Fill the owned column from the hardware quote and the facility quote: five machines and a spare over sixty months, the quarter rack, committed power, transit, the cross-connect, remote hands.
- 04 Add the salary line to BOTH columns, because both columns have one. The cloud estate already costs somebody sixty hours a month — the managed cluster upgrades itself on somebody's Tuesday, the credentials rotate, the bill gets argued with, the pager gets carried — and a cloud invoice bills for none of it. Owning adds about twenty hours a month on top of that, not a second person. Write both down. A column with the salary on one side only is not a comparison, whichever side it is missing from.
- 05 Add the line that does not come home. Move 04 settles which capabilities you keep renting — the edge, outbound mail, scrubbing — and there is a residue besides: archived object storage nobody will pay the egress to extract, a registry, a queue, an off-site backup copy. It is inside the rented column already, so it has to be inside the owned column too. Leaving it out is the same error as leaving out the salary, and it is worth about a tenth of the bill.
- 06 Total both columns and apply the rule. If owned is not a third under rented, stop and keep the spreadsheet. Stopping costs three Moves and a week, against a programme abandoned in month five with two estates billing.
- 07 If it clears, put the capital question to the founder who signs. About \$87,000 leaves the bank before anything serves a request — six machines and a pair of switches, and on eighteen months of runway that is a fair refusal; renting dedicated machines by the month is the way round it, in Move 07.

ROLLBACK

Nothing is ordered and nothing signed, so this Move reverses by changing a cell. The point of no return is the order in Move 06 and the contract in Move 07. Keep dated versions of the sheet, so earlier assumptions can be restored when somebody asks how the decision was reached.



04 THE THREE THINGS YOU KEEP RENTING

CUTOVER

0 MIN



LAYER DECIDE	LEAVING NOTHING — THIS MOVE DECIDES WHAT STAYS RENTED	RISK LOW	REVERSIBLE IMMEDIATELY
-----------------	--	-------------	---------------------------

Three capabilities do not come home: the edge, outbound mail and volumetric scrubbing. Naming them now keeps the plan honest.

AWS	CloudFront and Shield	Shield Advanced bills \$3,000 a month on a twelve-month term and attaches only to AWS resources, so it protects a distribution and never a rack.
GOOGLE	Cloud CDN and Cloud Armor	Cloud CDN is a mode on a load balancer backend, so a colocated origin must first become an internet network endpoint group.
AZURE	Front Door and its web application firewall	managed rule sets need the Premium tier, and the firewall policy is a resource that outlives its profile.

BEFORE YOU START

ACCESS

- The three invoice lines for edge, mail and mitigation, and authority to sign

SOFTWARE

- The comparison from Move 03, open for a new permanent line
- The sending domain's current SPF, DKIM and DMARC records

PEOPLE

- Whoever owns the marketing sends, who shares the reputation
- An engineer willing to name the fourth item honestly

WHY THIS WORKS

A plan that pretends everything comes home fails in Stage 5, when somebody notices password resets landing in spam folders and no schedule is left. Three capabilities are bought rather than built, because building them badly is worse than renting them well: a hundred points of presence, a decade of sender reputation, and absorption capacity upstream of your transit. None is expensive next to what it prevents, and all three are worth paying for after the move on the terms you pay now. Deciding here costs two days and removes the largest late surprise.

SWAP

One vendor covering delivery and mitigation halves the contracts, and one outage then takes both.

DO IT FASTER

Ask each vendor for the contract and onboarding checklist in the first message.

WATCH OUT

Facility-included protection is often a null route with a better name. Get in writing what it does to your address.

LEFTOVERS

The cloud edge stays in front of the cloud origin until Move 18 shifts traffic, so two edge bills overlap.

\$1,400/mo WAS	\$1,400/mo NOW	0% SAVED	0 min CUTOVER	2 days EFFORT	— WAIT
-------------------	-------------------	-------------	------------------	------------------	-----------

TURN OFF Nothing, and that is the point. The cloud's versions switch off in Moves 18 and 20; these three stay on the invoice permanently.

NEEDS 02 What you actually run 03 The number that decides it

THE RUNBOOK

- 01 | Price the edge. Take the delivery and egress figures off the invoice from Move 01 and quote three independent vendors against that volume. A content network in front of a rack is the same arrangement as in front of the cloud.
- 02 | Price outbound mail on its own. Transactional sending goes to a provider whose only business is deliverability, and the sending domain's SPF, DKIM and DMARC records point at it. Marketing sends take a separate subdomain.
- 03 | Price mitigation upstream of your transit, the only place it works. Ask the facility and each transit vendor what is included, at what capacity and how it triggers: a hundred-gigabit attack against a ten-gigabit port is decided before it reaches your equipment.
- 04 | Sign all three contracts before the hardware ships, confirming each notice period and minimum term. Mail warm-up takes weeks and cannot begin during an incident.
- 05 | Write the total, about \$1,400 a month, into the comparison from Move 03 as a permanent line. Then name the fourth item: whatever the business depends on that nobody here has run, such as a payments integration.

ROLLBACK

Nothing here touches a running system, so backing out is cancelling inside a notice period. The point of no return arrives later, when the sending domain's records point at the new provider: reputation then accrues on their addresses, and the old standing cannot be restored by changing the records back.



II BUY

What to order and where to put it. Nothing here is software, and getting it wrong is the only mistake in this book you cannot fix with a deploy. Both clocks start in this stage, and they run in parallel.

4 MOVES	4 ZERO DOWNTIME	2 HIGH RISK	0 MINUTES, TOTAL
------------	--------------------	----------------	---------------------

IF YOU ONLY DO THREE

05

FROM RENTED VCPUS TO CORES YOU OWN

Two vCPUs is one physical core, and the second thread is worth about a quarter of the first — the gap between five …

06

FIVE MACHINES, AND THE ONE ON THE SHELF

Three nodes is a quorum; five survives losing one; the sixth is bought with them and never plugged in, because iron …

FROM RENTED VCPUS TO CORES YOU OWN · FIVE MACHINES, AND THE ONE ON THE SHELF · A CAGE, NOT A DATA CENTRE · THE ORDER, AND THE WEEKS YOU CANNOT COMPRESS

■ 2 MEDIUM RISK

■ 2 HIGH RISK

05 FROM RENTED VCPUS TO CORES YOU OWN

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
BUY	THE VCPU AS A UNIT OF PURCHASE	MEDIUM	UNTIL THE ORDER IS SIGNED

Two vCPUs is one physical core, and the second thread is worth about a quarter of the first — the gap between five machines and nine.

AWS	EC2 instance types	a vCPU is one SMT thread on the x86 families but a whole physical core on Graviton, labelled the same.
GOOGLE	Compute Engine machine types	custom shapes set memory apart from cores, within a per-core band that drags cores onto the bill.
AZURE	Virtual Machine sizes	the B-series meters CPU against a credit balance, so a saturated workload reads low once its credits run out.

BEFORE YOU START

ACCESS

- The two-week measurement window from Move 01, working set sampled apart from CPU
- The instance inventory from Move 02, exported with family and size

SOFTWARE

- A sizing sheet other people can check, with the derate and headroom visible
- The vendor documentation for each instance family you run

PEOPLE

- Whoever signs the order in Move 06, present for the derate rather than shown it

WHY THIS WORKS

Move 01's samples become a part number here. The first conversion is the one nobody writes down: on x86 a vCPU is one hyperthread, so two share a physical core, and the second thread is worth fifteen to thirty per cent of the first, not another hundred. A 96-vCPU estate is a 48-core estate, which fits in two of these machines. Then three rules in order: memory, the ceiling a node reaches; clock, because a query plan runs mostly on one core; flash, because local NVMe beats rented block storage by orders of magnitude.

SWAP

With the window unfinished, size against last quarter's billed peak and mark the sheet provisional. It lands a third high.

DO IT FASTER

Most estates run five workload shapes wearing forty names. Cluster them and the conversion takes an afternoon.

WATCH OUT

Rightsizing advice optimises for a smaller rented instance, a different question from how much silicon to own.

LEFTOVERS

Local NVMe delivers the provisioned IOPS line as a property of the drive. Check it against your measured write rate.

—	—	—	0 min	3 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing yet, though the re-measurement in step two usually finds a service two sizes above its demand — shrink it and the bill falls this month.

NEEDS 01 The bill, and the three lines that are most of it 03 The number that decides it

THE RUNBOOK

- 01 Group the instance inventory by family and mark each thread-per-vCPU or core-per-vCPU against the vendor documentation. On Graviton and the other Arm shapes a vCPU is already a whole core, and halving buys double.
- 02 Pull the burstable families out of the measurement window. B-series and t3 in standard mode meter against a credit balance, and once the balance is empty a saturated workload pins at its baseline — twenty per cent on a t3.medium. t3 defaults to unlimited mode, where the number is honest and the burst above baseline arrives on the invoice instead. Re-measure either way before the figure reaches the sizing sheet.
- 03 Halve the thread groups and credit the second thread with the fraction it is worth. Record which peak you sized against: you paid for peak every hour of the month, and owned iron carries peak by definition.
- 04 Size memory from the working set plus kubelet reserve, page cache and the eviction threshold, then round up to a population that fills every channel. A node cannot be widened while it runs.
- 05 Take clock over count on the latency path — most of a Postgres query plan executes on one core — then turn capacity and write rate into drives and hand the specification to whoever signs the order in Move 06.

ROLLBACK

A specification is undone by writing a better one: change the derate and reissue it. Nothing has been bought. The point of no return is the signature in Move 06, after which a short memory line is a second purchase with a lead time. Keep the sheet in version control so a revision can be restored.

06 FIVE MACHINES, AND THE ONE ON THE SHELF

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
BUY	ELASTIC NODE CAPACITY AND CLUSTER AUTOSCALING	HIGH	UNTIL THE ORDER IS SIGNED

Three nodes is a quorum; five survives losing one; the sixth is bought with them and never plugged in, because iron does not autoscale

AWS	EC2 Auto Scaling groups	the fleet ceiling is a per-region vCPU quota, raised by support ticket.
GOOGLE	Managed instance groups	the instance template is immutable, so a shape change means a rolling replace.
AZURE	Virtual Machine Scale Sets	the platform fault domain count is fixed at creation and cannot be edited.

BEFORE YOU START

ACCESS

- The per-node sizing from Move 05 and the service inventory from Move 02
- Authority to raise a purchase order in the tens of thousands

SOFTWARE

- A quote comparison sheet with three vendors priced line by line

PEOPLE

- A vendor account manager who will price a configured node, not a parts list
- Whoever signs capital expenditure, warned four weeks ahead

WHY THIS WORKS

Five is the smallest fleet that makes the arithmetic of failure tolerable. Three nodes give a control plane its quorum and nothing more: lose one and a third of the capacity goes, while the survivors carry a load nobody sized them for. At five, a dead machine costs twenty per cent. The sixth is not in the rack. It is built, burned in, configured identically and then unplugged, because the replacement path left behind was an API call and the one ahead is a return authorisation and three weeks. Those weeks cost more than the machine that prevents them.

SWAP

Lease the six machines over three years. The total is higher, but the monthly line resembles the cloud bill it replaces.

DO IT FASTER

Ask for a configuration the vendor stocks. Wanting 288 GB because the model said 240 turns a two-week delivery into an eight-week build.

WATCH OUT

Rails, power leads, 25 GbE optics and the support contract are quoted separately. A bill of materials listing only servers is short by thousands.

LEFTOVERS

A spare helps only if it stays current. Firmware and the Talos version drift within a quarter, so the shelf machine boots and updates with the rest.

—	—	—	0 min	3 days	4 weeks
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing for months. The EC2 Auto Scaling groups carry production until Move 18 shifts the traffic; this Move only commits money.

NEEDS 02 What you actually run 05 From rented vCPUs to cores you own

THE RUNBOOK

- 01 Put the per-node sizing from Move 05 beside the service inventory from Move 02, add one whole machine of failure headroom, and divide by what a node holds. The reference estate lands on five.
- 02 Write the specification on one page: dual-socket, 32 physical cores, 256 GB of ECC memory with every channel populated, four 3.84 TB mixed-use NVMe drives plus a mirrored boot pair, redundant power supplies, two 25 GbE ports, and a controller speaking Redfish.
- 03 Send that page to three vendors, marking line by line what may be refurbished: chassis and processors two generations old run Kubernetes as well as new ones at half the price, while drives and power supplies wear and are bought new. Take each quote into the comparison sheet, ship date beside price.
- 04 Add the sixth node, identical to the other five: burned in with the rest, then pulled and shelved. It is the only capacity on site that does not arrive by courier.
- 05 Raise the purchase order, have the person who signs capital expenditure sign it, and put the ship date in the calendar. Moves 07 and 08 run against that date.

ROLLBACK

Everything before the purchase order is a document, and an unaccepted quote expires harmlessly. The point of no return is the signature: configured servers are built to order and rarely returnable. Afterwards they still hold about half their value second-hand.

07 A CAGE, NOT A DATA CENTRE

CUTOVER

0 MIN

LAYER	LEAVING	RISK	REVERSIBLE
BUY	THE REGION-AND-ZONE ABSTRACTION	HIGH	UNTIL THE CONTRACT IS SIGNED

A quarter rack ninety minutes from somebody who can drive to it, and the first line in this programme that costs money instead of saving it.

AWS	Regions and Availability Zones	zone letters are shuffled per account, so one account's us-east-1a is another's us-east-1c, and cross-zone traffic bills both ways.
GOOGLE	regions and zones	a subnet covers the whole region rather than a zone, and quota is granted per region, so capacity in one zone is not capacity in the next.
AZURE	regions, availability zones and zone-redundant tiers	zone support varies by region and by machine series, and a resource created without a zone cannot be moved into one later.

BEFORE YOU START

ACCESS

- The committed power figure and machine count from Move 06
- Quotations from three facilities against one written specification

SOFTWARE

- A comparison sheet with monthly charge, cross-connect price and notice period side by side

PEOPLE

- Two named people who can reach the building out of hours
- Whoever signs the term, before the price is agreed

WHY THIS WORKS

A region and a zone were labels on an invoice. Underneath sat a building, a power feed, a loading dock and somebody's hands, and this Move buys the smallest version of all four: a quarter rack in a carrier-neutral facility, near enough that somebody can be at the cabinet within a couple of hours. Nothing binds until a signature, and every term that hurts later is negotiable before it. It also costs more rather than less — about \$1,400 a month for the space, the transit, the cross-connect and the hands, paid from handover, before a machine is racked. One site, not two.

SWAP

Rented dedicated servers skip this Move and Move 08's lead times — about a month off the programme. Compare whole columns, not the hardware line against a column: rented metal costs somewhere between three-quarters and twice the \$3,235 of owned infrastructure depending on whose list you quote, and it wins back about a quarter of an engineer, so the totals land between comfortably under owning and level with it. What you give up is the network, your own addresses and the price you can hold; what you keep is the capital. On short runway, rent.

DO IT FASTER

Ask for the standard agreement and the cross-connect list before price is discussed; a day of reading decides which clauses are worth arguing.

WATCH OUT

A second building doubles the hardware, the spares and the change surface, and is the commonest reason a repatriation stalls. One site with backups held elsewhere beats two nobody has exercised.

LEFTOVERS

The cage invoices from handover while the cloud bill stays where it was; both run in parallel for about four months.

—	\$1,400/mo	—	0 min	4 days	3 weeks
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing. This Move adds an outgoing instead of removing one; the cloud bill does not move until the first service does.

NEEDS 03 The number that decides it

THE RUNBOOK

- 01 Write one specification — quarter rack, committed kilowatts, two feeds, cross-connects, remote hands, term — and send it to three facilities within ninety minutes' drive.
- 02 Size the power commitment against what actually draws: five racked nodes at about 450 W plus two switches is near 2.5 kW, and the eighty per cent rule means a 3 kW commitment only permits 2.4 kW continuously. Ask for 4 kW on two feeds from separate distribution boards, and leave the sixth machine unplugged on the shelf.
- 03 Put ticket-to-touch, the billing increment and a named escalation into the remote hands contract rather than the sales deck, and two named people on the access list so one holiday is not an outage.
- 04 Ask which carriers have live fibre in the meet-me room and which of them will sell at your volume, then get the cross-connect price list in writing, installation and disconnection included. Three carriers and a cheap cross-connect beat better marketing.
- 05 Negotiate the exit with the entrance: a term no longer than the hardware life, a capped escalator, a notice period you could serve. Three years with twelve months' notice repeats the mistake you are here to correct.
- 06 Before anyone signs, price the alternative in the next column of the comparison sheet: the same six machines rented by the month, racked and powered by somebody else. Quote it rather than taking a figure from here — the spread between the cheapest European provider and a US one is a factor of two or three on the same specification, and it is wide enough to decide the question on its own. At this fleet size that column is at worst competitive, and Move 03's rule applies to it too.

ROLLBACK

Refusing a facility that will not put ticket-to-touch in writing costs nothing: before signature there is no position to unwind. The point of no return is the commencement date, after which departure runs on the notice period rather than on a decision. File the quotations that lost; at renewal they restore a price to argue from.



08 THE ORDER, AND THE WEEKS YOU CANNOT COMPRESS

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
BUY	PROVIDER-ASSIGNED ADDRESSES AND MANAGED TRANSIT	MEDIUM	UNTIL THE ORDER IS SIGNED

Everything with a lead time goes on one order this afternoon, so the queues run beside each other instead of one after another.

AWS	Elastic IP and Direct Connect	the cross-connect authorisation expires ninety days after issue, and an Elastic IP bills on after its instance is gone.
GOOGLE	external IP and Cloud Interconnect	the partner variant hides the physical layer, so there is no cross-connect to order and capacity comes from a fixed list.
AZURE	Public IP and ExpressRoute	the circuit bills from creation, before the carrier has provisioned anything against its service key.

BEFORE YOU START

ACCESS

- The signed facility agreement from Move 07 and its cross-connect price list
- Purchase authority to sign transit and circuits

SOFTWARE

- The switch part numbers from Move 06, for the optic compatibility list
- A written order sheet, one promised date and one name per line

PEOPLE

- A named technical contact the carriers can reach in week three

WHY THIS WORKS

Every other stage of this migration is work you control. This one is queueing, and the only thing you control is when it starts. A cross-connect and an optic ordered in the same week arrive while the machines are being built; ordered in sequence they add a month each. So the whole list goes in on one afternoon, and you accept paying for two transit paths from the start, because one upstream is a single point of failure with a contract attached. Nothing is installed yet, so every line can be withdrawn up to signature.

SWAP

Buy every line from the facility on one invoice. It costs more per megabit and takes four vendors off the critical path.

DO IT FASTER

Ask for the authorisation templates before the agreement is countersigned; no queue starts until they are lodged.

WATCH OUT

A cloud's interconnect paperwork expires if the cross-connect is not done inside ninety days, and it is re-issued rather than extended.

LEFTOVERS

The blended transit stays on the invoice until your own circuit has carried a full month including a peak.

—	—	—	0 min	3 days	4 weeks
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing yet — this Move only adds lines. The first it retires is the blended transit, once your own upstream has held a month.

NEEDS 07 A cage, not a data centre

THE RUNBOOK

- 01 Order the cross-connects the day the facility agreement is countersigned: one per upstream, one for the out-of-band line, one spare. Ask whether the panels to the meet-me room are in place; that decides days against weeks.
- 02 Take the facility's blended transit for go-live, already in the building, and order a second upstream from a carrier on a different fibre route to run beside it. On the facility's own addresses that second circuit buys a price and a path to grow into rather than a failover, because only the facility's transit routes to you; it becomes a failover the day you announce your own prefix to both.
- 03 Take a /24 or a /25 and IPv6 from the facility. Your own autonomous system number can wait until a second site earns its eight weeks of registry paperwork. Rented space is a renumbering you may do twice.
- 04 Order the out-of-band line: a small separate circuit, or a mobile router. It is the cheapest item here and the one that matters at three in the morning.
- 05 Order optics and cables from the switch vendor's supported list, twenty per cent over the port count. Then chase the order sheet weekly.

ROLLBACK

Until a signature this Move is undone by an email. The point of no return is the first signed term, not the first delivery: transit and cross-connects carry minimum terms in months, and a circuit against the wrong cabinet is paid for whether or not it is lit. Keep the quotes in version control, so a position can be restored at renewal.

III BUILD

Everything between a racked machine and a cluster that could take production traffic. Nothing here moves a workload; all of it decides how well the rest of the book goes.

4 MOVES	4 ZERO DOWNTIME	3 HIGH RISK	0 MINUTES, TOTAL
------------	--------------------	----------------	---------------------

IF YOU ONLY DO THREE

09

RACKING DAY

Six boxes become six machines reachable from a hotel room. Rails, power and labels take the day; the proof takes 8hellip;

12

DISKS: WHAT GOES LOCAL, WHAT GOES ON CEPH

Ceph takes three drives a node for anything that must survive a node dying. The fourth stays raw under PostgreSQL 8hellip;

10

THE NETWORK, AND THE WAY BACK IN WHEN IT BREAKS

Four address ranges written down before anything is configured, two switches either of which may fail, and a way in 8hellip;

RACKING DAY · THE NETWORK, AND THE WAY BACK IN WHEN IT BREAKS · A CLUSTER, IN AN AFTERNOON · DISKS: WHAT GOES LOCAL, WHAT GOES ON CEPH

■ 1 MEDIUM RISK

■ 3 HIGH RISK



LAYER	LEAVING	RISK	REVERSIBLE
BUILD	THE PROVIDER'S SERIAL CONSOLE AND BOOT DIAGNOSTICS	MEDIUM	IMMEDIATELY

Six boxes become six machines reachable from a hotel room. Rails, power and labels take the day; the proof takes twenty minutes.

AWS	EC2 Serial Console	granted per account, Nitro types only, and no virtual media, so your own image never boots.
GOOGLE	Compute Engine serial console	switched on by the serial-port-enable metadata key, and an organisation policy can forbid it estate-wide.
AZURE	Boot diagnostics and Serial Console	on by default against a managed storage account you cannot open, gated behind a role and killable subscription-wide, and reaches the guest only, never wedged firmware.

BEFORE YOU START

ACCESS

- A booked day on site for two named people
- An out-of-band line that is live and independent of the uplinks

SOFTWARE

- `ipmitool` and a Redfish client on a laptop outside the building
- A memory tester, a drive exerciser and one firmware bundle for the whole batch

PEOPLE

- Two people for the lift; a chassis at head height is not a one-person job

WHY THIS WORKS

The physical work is ordered so nothing has to be undone: rails across all six positions before a chassis is lifted, weight low, power split so one distribution unit cannot take the estate. None of that is the point. The Move exists for the baseboard management controller in each node — a small computer with its own processor, port and firmware, and the whole of the console the cloud gave you. Proved from outside the building, it turns two years of faults into an afternoon at a keyboard rather than a drive to the facility.

SWAP

Remote hands will rack and cable to a drawing at about \$150 an hour; buy that for the lifting, not the controllers.

DO IT FASTER

Address and password the controllers on a bench the week before, so the day itself is cabling and testing.

WATCH OUT

Controllers answer on any interface they find; one reachable from the internet is a full-power console for a stranger.

LEFTOVERS

Cardboard, the spare's rail kit, and the temporary address scope that hands out addresses for months.

—	—	—	0 min	4 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing yet. Six machines draw power in one building while the whole cloud bill runs in another.

NEEDS 06 Five machines, and the one on the shelf 08 The order, and the weeks you cannot compress

THE RUNBOOK

- 01 Fit all six rail pairs before any chassis goes in, checked against the cabinet's depth. Rack bottom-up, heaviest low, two people on each lift.
- 02 A-side power from one distribution unit, B-side from the other, so a node's supplies never share a strip. Pull one feed per node and confirm it stays up.
- 03 Cable data in one colour and management in another, both ends labelled before anything is plugged in. Label the position, not the machine.
- 04 Give each controller a static address on the management VLAN, serial-over-LAN on, and a password the cluster cannot reach. Run each operation through `ipmitool` and Redfish, noting which answers.
- 05 Leave the building. From a laptop elsewhere, over the out-of-band line, watch a node POST, enter firmware setup, mount an image over virtual media and power-cycle it. Until that works from outside, nothing here is built.
- 06 Run the memory tester and the drive exerciser overnight on all six nodes, level them all to one firmware bundle, and before leaving site take front and rear photographs, the port map and a file naming which node is in which rack unit.

ROLLBACK

Nothing here carries data: a mistake is undone by unracking a machine the same afternoon. The point of no return is the day this cabinet takes production traffic, after which moving a cable is a change window. Firmware is the exception — a downgrade is sometimes refused, so record the shipped version per serial and keep the vendor's image so a working level can be restored.

10 THE NETWORK, AND THE WAY BACK IN WHEN IT BREAKS

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
BUILD	CLOUD-MANAGED PRIVATE NETWORKING	HIGH	IMMEDIATELY

Four address ranges written down before anything is configured, two switches either of which may fail, and a way in that depends on neither.

AWS	VPC and its subnets	a subnet is pinned to one Availability Zone and its block is fixed at creation, and frames run at 9001 bytes inside the VPC but 1500 through the internet gateway.
GOOGLE	VPC networks and subnets	the MTU belongs to the network rather than the instance, and every virtual machine must be restarted before it uses a changed value.
AZURE	Virtual Network and its subnets	no broadcast or multicast on the wire, so gratuitous ARP and VRRP never worked and a floating address had to be a load balancer.

BEFORE YOU START

ACCESS

- Console access to both switches, and the out-of-band line from Move 09 answering
- The public address range from Move 08, and the private ranges the organisation already uses

SOFTWARE

- `ipmitool` 1.8.19 or newer, to prove the baseboard controllers answer on the management range
- A packet test that sets the do-not-fragment bit, because a default-size ping proves nothing here

PEOPLE

- Two engineers for the switch-pull drill, one at the rack and one watching the graphs

WHY THIS WORKS

The address plan is cheap to get right today and expensive to change in a year, because by then it sits in a partner's firewall and on every machine. It is written first, on paper: four ranges, each with twice the room the estate needs now. The switches come as a pair, since one switch is one maintenance window that takes everything down with it. MTU gets a step of its own, because a mismatch does not fail cleanly — it passes small requests and stalls large ones. Nothing here carries production traffic yet, which is what makes the week safe.

SWAP

Where the switches will not do multi-chassis aggregation, give each node an address per uplink and let it route to both independently: more host configuration, fewer shared failure modes.

DO IT FASTER

Generate both switch configurations from the address plan rather than typing them twice. Hand-built pairs differ in one port, and the drill is what finds it.

WATCH OUT

The way back in must not depend on the fabric it exists to rescue. A jump host on the data VLAN, or a mesh agent that needs the production default route, is neither.

LEFTOVERS

The cloud private network and its per-gigabyte charges keep running throughout, and nothing here removes them.

—	—	—	0 min	4 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing yet. The cloud's private network carries every service you run until the traffic moves in Stage 5.

NEEDS 09 Racking day

THE RUNBOOK

- 01 Write the address plan before touching a switch. Four ranges — management, storage, node addressing and the public block from Move 08 — none overlapping the office, the cloud accounts or anything a partner routes. It lives in source control and nowhere else.
- 02 Cable the two top-of-rack switches as a multi-chassis pair with a peer link, and run two uplinks from every node into different switches, bonded. One switch then fails as a component rather than as an outage.
- 03 Build the management VLAN with no route to the internet. The baseboard controllers and the out-of-band circuit sit on it, and the way in is a jump host, never a public address. Prove it from outside the building with an `ipmitool` power status on every node.
- 04 Set the MTU identically on every switch port, every bond and every node, and record the number beside the address plan. Undocumented mixed segments are how a fortnight disappears.
- 05 Test with full-size packets that refuse fragmentation, on every path that will carry traffic. A mismatch breaks about five per cent of it and reads as an application bug for a week.
- 06 Run the drill in daylight, with both engineers watching. Pull the power from one switch, confirm every bond keeps a member, then plug it back in and confirm the link rejoins. Nobody who declines this today will do it under load.

ROLLBACK

Nothing here carries production traffic, so backing out is reverting one switch configuration and restoring the previous one from source control. The point of no return is a date rather than a command: once node addresses and partner firewall entries reference the plan from step one, renumbering becomes a weekend rather than an edit. Argue the ranges into shape now, not after Move 11.



11 A CLUSTER, IN AN AFTERNOON

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
 BUILD	THE MANAGED KUBERNETES CONTROL PLANE	 HIGH	IMMEDIATELY

The frightening part is the short part: six machines, one file in Git, and an operating system with no shell to log into.

AWS	EKS	tearing a cluster down leaves its IAM OIDC provider behind, still trusting an issuer URL nothing resolves.
GOOGLE	GKE	the control plane upgrades on its release channel regardless; a full-freeze exclusion cannot exceed 90 days, and holding a minor version only lasts until that version leaves support.
AZURE	AKS	the Free tier carries no API server uptime guarantee at all, so what is given up is a paid Standard tier or nothing at all.

BEFORE YOU START

ACCESS

- The six machines from Move 10, powered and reachable on the management VLAN
- One unused address on the server VLAN, for the API virtual IP

SOFTWARE

- `talosctl` and `kubect` at the same minor version as the cluster you are building
- `helm` and the Cilium chart pinned to an exact chart version, not a range
- The cilium CLI, for the connectivity test

PEOPLE

- Someone to power a machine off at the wall while another watches the API

WHY THIS WORKS

A control plane is three machines that agree with each other, and the agreement is etcd. Talos Linux removes the reason hand-built clusters rot: no shell, no package manager, no login, so changing a machine means changing the YAML in Git and applying it. Drift stops being a category. Doing this while nothing runs is what makes the risk survivable — every mistake costs a rebuild, and an empty cluster rebuilds in twenty minutes. Be plain about the money: a managed control plane is about \$73 a month — the same ten cents an hour on all three — so this is not the Move that pays for the migration.

SWAP

If replacing kube-proxy on day one is a step too far, run Cilium alongside it and take kube-proxy out a week later.

DO IT FASTER

Build the cluster twice from the same commit. The second build takes twenty minutes and shows whether the first was reproducible or lucky.

WATCH OUT

On flash without power-loss protection, etcd throws leader elections under write load, which reads as an intermittent network fault.

LEFTOVERS

Write the upgrade cadence down today — one minor behind, reviewed quarterly. Nobody picks it calmly once a version is out of support.

\$73/mo	\$0/mo	100%	0 min	4 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing yet — the managed cluster still carries production and stays until Move 20. Its per-hour control-plane charge is the first bill line to reach zero.

NEEDS 10 The network, and the way back in when it breaks

THE RUNBOOK

- 01 Commit the machine configuration before applying it. Generate the base with `talosctl gen config`, pin the Kubernetes version one minor behind the newest, point the API endpoint at the virtual address on the server VLAN, and give etcd a partition on its own NVMe device — every etcd commit is an fsync, and nothing doing bulk writes shares that device.
- 02 Apply it to the three control-plane machines and run `talosctl bootstrap` on one. The installer wipes and repartitions the target disk, so confirm each machine's serial against the rack map first.
- 03 Join the rest. Two become workers; the sixth takes the same configuration and stays cordoned, so replacing a dead node is an uncordon rather than a build. Leave the control-plane nodes schedulable — six machines cannot spare three that only run etcd.
- 04 Install Cilium with `helm install` at the pinned chart version, kube-proxy replacement on, and the API host set to the virtual address, never a name: a name needs DNS, and DNS needs the network this step builds. Disable kube-proxy in the machine configuration in the same commit.
- 05 Verify with `kubectx` that no kube-proxy service chains survive on any node, then run the cilium connectivity test and read all of its output.
- 06 The acceptance test: pull the power on one machine at random, watch the API stay reachable and the pods reschedule, then power it back on and confirm it rejoins untouched. Do it while the cluster is empty; that is the last time it is cheap.

ROLLBACK

While the cluster is empty nothing here is hard to undo. Reverting the kube-proxy flag in the machine configuration and reapplying it takes a minute: an enormous blast radius, and a way back that is one flag. The point of no return is Move 12, where the first volume binds to a machine. Keep every configuration version in Git so a known-good one can be restored exactly.



12 DISKS: WHAT GOES LOCAL, WHAT GOES ON CEPH

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
BUILD	MANAGED BLOCK AND SHARED-FILE STORAGE	HIGH	IMMEDIATELY

Ceph takes three drives a node for anything that must survive a node dying. The fourth stays raw under PostgreSQL, which already replicates itself.

AWS	EBS and EFS	a gp3 volume lives in one Availability Zone and caps at 16,000 IOPS however large it grows, and EFS in bursting mode spends credits that run out.
GOOGLE	Persistent Disk and Filestore	Persistent Disk performance scales with provisioned size and the attached machine's vCPU count, and a Filestore instance grows but never shrinks.
AZURE	Managed Disks and Azure Files	Premium SSD steps in fixed tier sizes rather than a dial, and premium file shares need a FileStorage account that standard shares cannot move into.

BEFORE YOU START

ACCESS

- The device inventory from Move 09, with the four NVMe drives on each node known by serial
- A Talos machine configuration you can edit and roll, because disk layout is fixed at boot

SOFTWARE

- `helm` and `kubectl`, with the Rook chart pinned rather than tracking whatever is newest
- `ceph` for health, capacity and recovery output during the drive-pull test

PEOPLE

- One named owner for Ceph, who will read its health output on the day it is unhappy

WHY THIS WORKS

Two storage systems, and one rule for choosing between them. Ceph, run by Rook, takes anything that must survive a node dying without waking anybody: replicated block volumes, a shared filesystem for the few things that need one, and the object gateway Move 15 and Move 16 build on. PostgreSQL takes the other path, a raw local drive with nothing replicating beneath it. The volume it used to sit on provisioned a few thousand IOPS; the four drives already in the machine will do several hundred thousand. A database writes copies to its own standbys, so a layer repeating that work underneath spends flash to buy nothing.

SWAP

A workload that must move between nodes freely and cannot replicate itself goes on Ceph block, latency included. The choice is which layer pays for replication.

DO IT FASTER

Name the storage classes for the promise they make, not the technology beneath. An engineer picking one is choosing durability, not a product.

WATCH OUT

Ceph says loudly that it is unwell and quietly why. Learn to read `ceph health detail` on a calm afternoon rather than during an outage.

LEFTOVERS

The managed volumes, file shares and their snapshots bill right through Stage 4. This Move stands the replacement up; it stops nothing.

\$2,100/mo	\$180/mo	91%	0 min	4 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing this week. The managed disks and shares carry production until Stage 4 moves what is on them; the line dies in Move 15 for the buckets and Move 16 for the database.

NEEDS 11 A cluster, in an afternoon

- 01 Name the owner for Ceph, then write the split into the Talos machine configuration: three of the four NVMe devices per node to Ceph, the fourth raw for PostgreSQL. Layout is fixed at boot, so changing it later means draining one node at a time.
- 02 Install Rook with `helm install rook-ceph rook-release/rook-ceph --version 1.16.9` and let the operator adopt the 15 devices offered. Take the Ceph release that chart version ships with, not the newest published.
- 03 Create a replicated block pool with three copies and `min_size 2`, a shared filesystem, and the object gateway on its own pool. Erasure coding does not belong under block storage on five nodes: too few failure domains, and a pool holding data will not take a different scheme later.
- 04 Size for recovery, not for today. Losing one node of five pushes a fifth of the data onto the survivors, so run `ceph df` and hold the pools under 70 per cent. Fuller than that, recovery backfills into a wall and writes start failing.
- 05 Bind a claim with `kubectl`, write to it, reboot the node beneath it and check the contents survived. Repeat on the shared filesystem, then create the first bucket on the gateway; Move 15 and Move 16 expect that endpoint already.
- 06 Pull a drive from a running node and time the recovery with `ceph -s`, once the claims above are verified and nothing real is bound. Reseat it and watch the cluster take it back. That number is what somebody works against the first time a device dies for real.

ROLLBACK

Nothing is bound yet, so removing Rook and handing the devices back is a morning's work — until the first claim binds or the first object lands in the gateway. That is the point of no return: after it, leaving Ceph is a data migration with a write stop, not a configuration change. Prove the way back before you get there — snapshot a test volume, delete the claim, restore it, confirm the contents match. The raw drives hold nothing until Move 16.

IV MOVE

The application first, then the state. The stage that can lose a company its data, and therefore the one with the longest overlap windows, the most rehearsal and the fewest one-way steps.

4 MOVES	3 ZERO DOWNTIME	2 HIGH RISK	15 MINUTES, TOTAL
------------	--------------------	----------------	----------------------

IF YOU ONLY DO THREE

13

IMAGES, SECRETS AND ONE-COMMAND DEPLOYS

Three pieces of plumbing, then staging moves onto them: the first real workload on hardware you own, and the only one …

15

BUCKETS, CACHE AND QUEUES

Objects, cache and queues move by copying to a second place, then changing an endpoint. None of them needs writes …

14

THE FIRST SERVICE, END TO END

The cheapest stateless service goes first, running on your hardware against the cloud database across the link, with …

IMAGES, SECRETS AND ONE-COMMAND DEPLOYS · THE FIRST SERVICE, END TO END · BUCKETS, CACHE AND QUEUES · POSTGRES, THE ONE THAT MATTERS

■ 2 MEDIUM RISK

■ 2 HIGH RISK

13 IMAGES, SECRETS AND ONE-COMMAND DEPLOYS

CUTOVER

0 MIN



LAYER MOVE	LEAVING MANAGED REGISTRIES, SECRET STORES AND HOSTED CI RUNNERS	RISK MEDIUM	REVERSIBLE IMMEDIATELY
---------------	--	----------------	---------------------------

Three pieces of plumbing, then staging moves onto them: the first real workload on hardware you own, and the only one whose bad afternoon costs you nothing.

AWS	ECR and Secrets Manager	the registry token expires every twelve hours, and a secret you remove holds its name for thirty days unless you ask for the seven-day minimum.
GOOGLE	Artifact Registry and Secret Manager	values are immutable, so every rotation leaves a billable version until destroyed.
AZURE	Container Registry and Key Vault	soft-delete cannot be switched off, and purge protection, once on, holds the name ninety days.

BEFORE YOU START

ACCESS

- A Git repository the cluster can read, with a deploy key held outside it
- An account on the registry you push to today, so the cache can pull private images

SOFTWARE

- Argo CD 3.0 and Harbor 2.12, both installed with Helm at pinned chart versions
- sops and age for encrypting secrets, with the private key kept off the cluster
- A runner controller for your forge, ephemeral rather than long-lived

PEOPLE

- One engineer who owns the repository layout; two owners produce two conventions

WHY THIS WORKS

Nothing real has moved yet, so this is the moment for plumbing. A registry you own makes a build that cannot reach its base image a problem you fix, not an outage you watch. Cluster state in a repository, reconciled by Argo CD, makes every Move that follows a commit, and a commit can be reverted. Secrets encrypted there, under a key held outside the cluster, mean a cluster rebuilt from bare metal gets its credentials back. Runners come last because they hold most of the \$640: hosted minutes bill by the minute, and a spiky build queue pays for waiting. Then staging goes, and it goes before anything a customer touches. This is the sequencing decision the whole stage rests on. Staging is a real workload — real images, real secrets, real deploys, real people who will tell you within the hour when it is wrong — and it is the only real workload whose bad afternoon appears on no invoice, breaches no agreement and wakes nobody. Every class of problem the platform has, it has under staging first: a storage class that does not bind, a network policy nobody wrote down, a base image that only existed in a cache, a deploy that works once and not twice. You would rather find those with your own engineers complaining in a channel than with Move 14's production service in front of users. It is also the honest rehearsal for the ones after it, because a staging estate is usually the same shapes as production at a tenth of the size.

SWAP

A plain registry over the same object store drops the database and cache Harbor needs, and with them projects, quotas and scanning.

DO IT FASTER

Do the cache in an afternoon and leave the registry of record a fortnight; most of the benefit arrives with the first half.

WATCH OUT

The registry has to run for the cluster to start, and the cluster for the registry to serve. Power the rack down and up once, deliberately, before an outage asks it.

WATCH OUT

Staging that still talks to production data stores has not moved, it has been relocated. Point it at its own copies before step seven.

LEFTOVERS

The cloud registry bills storage and egress until its images go, a Move 20 decision, and hosted runner minutes continue for anything still routed at them.

\$640/mo WAS	\$60/mo NOW	91% SAVED	0 min CUTOVER	5 days EFFORT	2 weeks WAIT
-----------------	----------------	--------------	------------------	------------------	-----------------

TURN OFF The hosted runner minutes, once a week of builds has passed on your own nodes with no fallback. The non-production estate's cloud compute, once the fortnight in step seven is done and nobody has asked to go back. The cloud registry and its secret store stay funded until Move 20.

NEEDS 11 A cluster, in an afternoon 12 Disks: what goes local, what goes on Ceph

THE RUNBOOK

- 01 Stand the registry up as a cache. `helm install` Harbor at chart version 1.16.2 on the Ceph object store from Move 12, proxying the registry you use today. Repoint pulls and confirm workloads still start.
- 02 Make it where images are pushed. Move the pipeline's push target across and mirror ninety days of tags, so both registries hold the same images while yours is on trial.
- 03 Put the cluster in the repository. `helm install` Argo CD at chart version 8.1.3, as an application of applications, so one path rebuilds namespaces, deployments, network policy and Move 12's storage classes. Bootstrap credentials come from outside the cluster.
- 04 Encrypt every secret into the same repository with `sops`, under an age key kept in a password manager and one offline copy. A rebuilt cluster is seeded with that key by hand; the key never lives inside the thing being rebuilt.
- 05 Delete a non-production namespace and let the reconciler put it back. Do this only after step four, and check the workload returns with its secrets attached.
- 06 Install the ephemeral runner controller at chart version 0.12.1 and route builds to it by label. Then the acceptance test: an engineer changes one line and the image builds, lands in your registry and deploys with nobody at a console.
- 07 Move the whole non-production estate — staging, review environments, whatever the branch builds deploy to — and leave it there. Point its DNS at the new cluster, let its data stay wherever it is for now, and tell the engineers who use it that it has moved and where to complain. Then use it: for a fortnight, every branch deploys here and nowhere else. The bugs this finds are the bugs Move 14 would otherwise find in front of users, and the cost of finding them here is somebody saying the preview is slow.

ROLLBACK

All of this is a repository: a bad change is a revert, and the reconciler catches up. Pulls point back at the cloud registry, builds back at hosted runners by one label. The point of no return is the day the cloud registry's images go, because a restore then means rebuilding from source, not pulling a tag. Keep the cloud secret store populated until a rebuilt cluster has decrypted its own secrets unaided.

14 THE FIRST SERVICE, END TO END

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
MOVE	MANAGED CONTAINER COMPUTE	MEDIUM	IMMEDIATELY

The cheapest stateless service goes first, running on your hardware against the cloud database across the link, with a DNS weight as the way back

AWS	ECS on Fargate	task credentials come from the metadata endpoint at 169.254.170.2, which does not exist on your nodes.
GOOGLE	Cloud Run	between requests the CPU is throttled to almost nothing unless it is always allocated, so idle timers stop firing.
AZURE	Container Apps	the outbound address belongs to the environment, not the app, so rebuilding it changes what partners must allowlist.

BEFORE YOU START

ACCESS

- Write access to the Argo CD repository holding the cluster's application manifests
- Permission to edit the weighted DNS records for the service's hostname

SOFTWARE

- kubectl and argocd, both already pointed at the new cluster
- dig for confirming what public resolvers return during the ramp

PEOPLE

- The service owner, told which week the ramp runs and what would stop it
- Whoever maintains egress allowlists on partner systems, warned in advance

WHY THIS WORKS

The first service to leave is chosen for how little it matters, because its job is to produce evidence rather than savings. Its database stays in the cloud, so the only new variables are the platform, the network path and the identity model. The link adds latency, and the number measured here decides which later services can live with a database on the far side of it and which must move in the same window as their data. The exit is a weighted DNS record: one value, one cache expiry. Nothing else returns as much for as little exposure.

SWAP

If the service sits behind a proxy you already control, shift weight there rather than in DNS; the abort is then immediate, not TTL-bound.

DO IT FASTER

Ramp on a Tuesday morning with the owner beside you. Two people reading one graph is most of what the first one is for.

WATCH OUT

A mean response time stays flat while one pod in four times out. Alert on percentiles and status codes, not averages.

LEFTOVERS

The old record sits at zero weight and the allowlists carry both ranges. Both are free and both get forgotten, so date each.

\$6,800/mo	\$0/mo	100%	0 min	10 days	1 week
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF The managed container service, its task revisions and its log retention — but not after the first service's week at full weight, which is the mistake this line used to invite. It goes when the LAST service off step 6 has held for a week, which is a week after the cadence ends rather than a week after it starts.

NEEDS 13 Images, secrets and one-command deploys

THE RUNBOOK

- 01 Choose the cheapest stateless service, not the most interesting one. The right candidate is one whose failure is a shrug and whose owner will not escalate over a slow hour.
- 02 Commit its manifests to the Argo CD repository and let `argocd` sync them. Keep the connection string on the cloud database, swap anything reading instance metadata for a real credential, and tell the partners who filter on egress addresses.
- 03 With no live traffic, drive synthetic requests at the new copy and compare latency percentiles against the cloud copy. Write the added milliseconds down.
- 04 Ramp the weighted record: one per cent, ten, fifty, all of it. Hold each step a business day, confirm the split with `dig`, and stop on any rise in error rate or the ninety-ninth percentile.
- 05 Soak a week at full weight, watching node disk with `kubectl`: scratch files that were ephemeral on the managed runtime still are, but now they fill a machine you own.
- 06 Then repeat across the stateless estate, two services a week. After the third, nobody asks for a plan. This is most of the Move: the first service is five days and the dozen behind it are about half a day each, which is what the strip books as effort. The five weeks of cadence are not booked twice — they are the calendar the ten days are spread across, not a window in which nobody works.

ROLLBACK

Every step before the ramp is additive: two copies exist and the cloud copy carries the traffic. Backing out is setting the weighted record to zero and waiting one TTL. There is no point of no return here — no state has moved, so there is nothing to restore. The exception is a partner's allowlist entry: leave the old address in place for the week.

15 BUCKETS, CACHE AND QUEUES

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
MOVE	MANAGED OBJECT STORAGE, REDIS AND QUEUES	HIGH	30 DAYS

Objects, cache and queues move by copying to a second place, then changing an endpoint. None of them needs writes stopped.

AWS	S3, ElastiCache and SQS	SQS now carries a megabyte a message, so a large payload may be sitting inline rather than as a pointer into a bucket.
GOOGLE	Cloud Storage, Memorystore and Pub/Sub	Pub/Sub acknowledges per subscription, so two subscriptions deliver everything twice.
AZURE	Blob Storage, Azure Cache for Redis and Service Bus	sessions and duplicate detection begin at the Standard tier; Basic has no topics.

BEFORE YOU START

ACCESS

- Read access to every bucket and the managed cache, and write on the Ceph gateway (Move 12)
- The queue inventory: visibility timeouts, dead-letter rules and message size ceilings

SOFTWARE

- rsync 1.68 or newer, comparing checksums rather than size and time
- Valkey 8.0 with valkey-cli, and NATS JetStream 2.10 with the nats command line

PEOPLE

- The owner of each key pattern and each queue consumer: both switches are code changes

WHY THIS WORKS

The database is the hard migration; this one runs beside it. Objects, cache and queues can each be written to two places at once, so the work is a copy repeated until the delta is boring, then a configuration change. Writes never stop. The risk is not the bytes but the assumptions in the code: an object store that promised more than the standard did, a cache holding sessions nobody labelled as state, a queue whose visibility timeout the consumer extends. Reading source finds those. Watching a transfer does not.

SWAP

One small bucket read by one service needs no repeated passes. Copy it once, verify it once.

DO IT FASTER

Start the bulk copy the week the cluster comes up. It is bandwidth, not attention, and the last delta takes an hour.

WATCH OUT

Presigned links issued before the endpoint changed resolve to the cloud until expiry; somebody always set one to a year.

LEFTOVERS

Non-current object versions bill on after the live ones go, and cache nodes bill until the last client moves.

\$2,900/mo	\$240/mo	92%	0 min	5 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF The cache nodes and the managed queues, after thirty days and a clean billing cycle. The object line shrinks rather than going: the archive stays.

NEEDS 12 Disks: what goes local, what goes on Ceph 14 The first service, end to end

THE RUNBOOK

- 01 | Sort the object estate by size and last access. Hot buckets move; archive stays, because egress on extracting terabytes exceeds years of its storage fee.
- 02 | Copy the hot buckets with `rc1one` onto the Ceph gateway, repeating until a pass takes minutes. A multipart entity tag is a digest of digests: it compares only if part sizes match.
- 03 | Change the endpoint, then run a last `rc1one` pass for what was written during the swap. Read the client code for listing order, read-after-write on overwrites, part size.
- 04 | Scan the cache key space by pattern. Patterns with no expiry are sessions, counters and locks — state, not cache — and wait for Move 16. The owner confirms; the rest point at Valkey 8.0, checked with `valkey-cli`, and take a cold start in a quiet hour.
- 05 | Stand up NATS JetStream 2.10 beside the old queues. Make consumers idempotent, then have producers write to both for a day, checking each visibility timeout against a long job.
- 06 | Drain the old queues to zero, watch `nats` take the load, then stop the old consumers. Both copies are retained for thirty days; nothing is deleted.

ROLLBACK

Nothing here is deleted, so backing out is three configuration changes: object endpoint, cache endpoint, broker. Objects written to Ceph afterwards are restored by copying the other way. The point of no return is the first message acknowledged only on the new broker.

16 POSTGRES, THE ONE THAT MATTERS

CUTOVER

15 MIN



LAYER	LEAVING	RISK	REVERSIBLE
MOVE	MANAGED POSTGRESQL	HIGH	7 DAYS

Fifteen minutes of stopped writes, at the end of a week in which the new cluster was caught up, backed up, and restored once on purpose.

AWS	RDS for PostgreSQL	the default parameter group cannot be edited, so <code>rds.logical_replication</code> needs a custom group and a reboot.
GOOGLE	Cloud SQL for PostgreSQL	storage auto-grows to hold retained write-ahead log and never shrinks, so it bills at the high-water mark.
AZURE	Database for PostgreSQL flexible server	<code>CREATE EXTENSION</code> fails until the name is in the <code>azure.extensions allowlist</code> , and anything wanting shared memory needs <code>shared_preload_libraries</code> too, which does need a restart.

BEFORE YOU START

ACCESS

- Logical decoding enabled on the managed instance, with the reboot taken
- Credentials for a bucket on the object gateway from Move 12, separate from the cluster's

SOFTWARE

- CloudNativePG 1.25 or newer, failed over by hand at least once already
- The Barman Cloud plugin for CloudNativePG, pinned, because the operator writes `archive_command` itself and will not take one from you
- `psql` and `pg_dump` no older than the managed server

PEOPLE

- The application owner, present for the window when writes stop

WHY THIS WORKS

Nothing here is new except the data. The local NVMe and the object gateway the backups go to both came up in Move 12, that gateway has carried the application's own buckets since Move 15, and the application has run on the cluster since Move 14. CloudNativePG supplies the part nobody wants to write: a primary, two standbys, and an operator that promotes one without a human awake at three in the morning. The copy is a stream, not a dump, so the new cluster is caught up and dull for days before anyone books a window. The rehearsed restore is what makes the fifteen minutes safe.

SWAP

Leave the managed instance subscribed to the new cluster for the week, replicating backwards. One more week of the old bill turns rollback into a repoint.

DO IT FASTER

Split the publication into several subscriptions grouped by table size, so the initial copy runs in parallel, not table by table.

WATCH OUT

Replication carries rows only. Sequences, large objects, schema changes and tuned parameters stay behind, and a sequence left at one collides on the first insert.

LEFTOVERS

The replication slot on the source outlives its subscription and retains write-ahead log for a reader that has gone.

\$4,900/mo	\$0/mo	100%	15 min	6 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF The managed instance, its read replicas and their snapshots, after the seven days and once an invoice shows the line gone.

NEEDS 12 Disks: what goes local, what goes on Ceph 13 Images, secrets and one-command deploys 15 Buckets, cache and queues

THE RUNBOOK

- 01 | List the extensions and roles on the managed instance with `psql`. What exists only on the provider's fork is replaced, re-expressed, or blocks the Move.
- 02 | Copy the schema with `pg_dump --schema-only` onto a CloudNativePG cluster of one primary and two standbys on local NVMe, deferring the biggest indexes.
- 03 | Create the logical replication publication and subscription and let it run for days. Read `pg_stat_subscription` each morning: a stalled subscriber fills the source's disk.
- 04 | Declare the object store as the cluster's backup destination so the Barman Cloud plugin drives it, turn on continuous archiving, watch the first write-ahead log segments arrive in the bucket, and only then take the full backup.
- 05 | Restore that backup into a scratch cluster, replay to a chosen timestamp, and count rows against production. Time it. The cutover waits until this passes.
- 06 | Open the window. Stop writes at the application, wait for lag to reach zero, advance every sequence, promote, repoint, start writes.

MOVE

ROLLBACK

Until writes resume, backing out is releasing the pause. The point of no return is the first commit on the new cluster: after that the two have diverged, and going back means replaying those writes or losing them. The managed instance stays up with its backups on for seven days, a copy that can still be restored to a timestamp.

V RUN

The traffic, the pager and the last account. Every article about leaving the cloud stops before this stage, and every migration that regrets itself failed inside it.

4	3	3	10
MOVES	ZERO DOWNTIME	HIGH RISK	MINUTES, TOTAL

IF YOU ONLY DO THREE

17

THE FRONT DOOR

The new edge goes up beside the one carrying users, with its own address and certificates, proved from a host file …

19

BACKUPS YOU HAVE RESTORED, AND THE PAGER

Velero, a continuous database archive and a copy somewhere you are not leaving — then the drill that turns a guessed …

18

GO-LIVE, AND HOW YOU ABORT

The weight moves in four steps and comes back in one, which is why the time-to-live drops a day early and the old …

THE FRONT DOOR · GO-LIVE, AND HOW YOU ABORT · BACKUPS YOU HAVE RESTORED, AND THE PAGER · CLOSING THE ACCOUNT

■ 1 MEDIUM RISK

■ 3 HIGH RISK

17 THE FRONT DOOR

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
RUN	MANAGED LAYER-7 BALANCERS AND CERTIFICATE SERVICES	MEDIUM	IMMEDIATELY

The new edge goes up beside the one carrying users, with its own address and certificates, proved from a host file entry while real traffic goes elsewhere.

AWS	Application Load Balancer and ACM	the validation record must stay in the zone forever, because every renewal re-checks it.
GOOGLE	external Application Load Balancer and Certificate Manager	URL map, target proxy and forwarding rule are separate objects, and the reserved address outlives all three.
AZURE	Application Gateway and Key Vault certificates	the gateway reads its certificate through a managed identity, and withdrawing that grant fails the gateway.

BEFORE YOU START

ACCESS

- The public address range from Move 08, with one address held back for the gateway
- Write access to the repository from Move 13, the one Argo CD reconciles
- An export of every listener rule, redirect, rewrite and health check from the managed balancer

SOFTWARE

- `helm`, with a pinned chart version for each of the two installs below
- `cmctl` and `openssl`, to check issuance and to read what a listener actually serves

PEOPLE

- Whoever owns the two most valuable transactions, to walk them end to end first

WHY THIS WORKS

An edge cannot be half-tested once it is live, so this one is built beside the live one. Envoy Gateway takes an address from the range ordered in Move 08, terminates its own certificates, and routes to the services Move 14 and Move 16 already put on your hardware. No user arrives, because no DNS record points at it. That exposes the hard part cheaply: the listener rules and rewrites accumulated in the managed balancer over three years, which nobody has a full list of. As Gateway API objects they can be read and diffed.

SWAP

Under a dozen rules, skip the table and write the routes directly. It earns its keep around thirty.

DO IT FASTER

Stand the gateway up against one low-traffic service and keep that route as a permanent smoke test. It exercises address, certificate and route before the table exists.

WATCH OUT

A renewed certificate and a reloaded one are different events. Envoy takes a new secret in seconds; a legacy proxy behind it may not. cert-manager renews at day sixty of a ninety-day certificate, so the stale copy stays valid for another thirty and the symptom arrives on day ninety.

LEFTOVERS

The managed balancer charges per hour and per capacity unit until Move 18, and its validation records must stay in the zone or its certificates stop renewing.

\$780/mo	\$90/mo	88%	0 min	4 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Nothing yet. The managed balancer, its listener rules and its certificate service switch off in Move 18, where the \$780 line stops.

NEEDS 14 The first service, end to end 16 Postgres, the one that matters

THE RUNBOOK

- 01 | Install both controllers with `helm` at fixed versions — `helm install eg oci://docker.io/envoyproxy/gateway-helm --version v1.4.2`, and `cert-manager` at `v1.17.2`. Commit the values to the repository so Argo CD owns them.
- 02 | Bind the gateway to one address from the Move 08 range as a virtual IP in layer-2 mode. Cut power to the node holding it and time the recovery: on one rack that is neighbour cache expiry, not anycast, and ten to thirty seconds is honest.
- 03 | Issue certificates through `cert-manager`, confirm with `cmctl status certificate`, then read what the listener serves using `openssl s_client -connect`. Prove renewal in a scratch cluster by winding its clock past the threshold, not by waiting until day eighty-nine.
- 04 | Read the balancer export line by line into a table: one row per listener rule, path condition, redirect, header rewrite, sticky-session setting and health check. The rule nobody remembers is the one a customer depends on.
- 05 | Translate each row into an `HTTPRoute` in the repository and write one request that proves it. Priority ordering and specificity ordering disagree, so a rule shadowed for two years comes back to life once translated faithfully.
- 06 | Point a laptop at the new address with a host file entry and walk sign-in, the two most valuable transactions, a large upload and any websocket. Cut nothing over; Move 18 moves the traffic.

ROLLBACK

Nothing here serves users, so backing out is removing the gateway objects and the address assignment, once no host file entry still points at them. There is no point of no return in this Move, by design. Keep the definitions in the repository so the edge can be restored in an afternoon.

18 GO-LIVE, AND HOW YOU ABORT

CUTOVER

10 MIN



LAYER	LEAVING	RISK	REVERSIBLE
RUN	WEIGHTED DNS AND THE PARALLEL MANAGED EDGE	HIGH	7 DAYS

The weight moves in four steps and comes back in one, which is why the time-to-live drops a day early and the old edge stays up a week.

AWS	Route 53 weighted records	a group weighted entirely to zero answers with every record in it, so drain by raising the survivor.
GOOGLE	Cloud DNS routing policies	a policy cannot coexist with a plain record of the same name and type, so creating one replaces that set.
AZURE	Azure DNS and Traffic Manager	weighting lives in the profile, not the zone, so the apex needs an alias record and a second time-to-live.

BEFORE YOU START

ACCESS

- Write access to the authoritative zone, and a second person who has it too
- The change window agreed with whoever answers the support line

SOFTWARE

- dig run from two networks you do not control, and a resolver you have never used
- argocd sync windows, or another way to hold every deployment for the day

PEOPLE

- One named decider, and the abort criteria they read out rather than argue

WHY THIS WORKS

Almost all of this Move is preparation, and the preparation is writing things down while nobody is under pressure. The mechanism is one field: a weight on a record, moved four times and movable back once. It is safe because the destination already carries real traffic and already holds the same rows as the source, so nothing is proved here for the first time. The time-to-live decides how long an abort takes, so it drops ahead of the day and is checked rather than assumed. Each soak spans a traffic cycle, because a filling connection table hides in a quiet minute.

SWAP

Where a contract forbids a freeze, run the ramp in the customer's quiet hours in smaller increments across a fortnight.

DO IT FASTER

Take the one per cent step a week early, on its own. It finds the certificate and header faults while there is time to fix them.

WATCH OUT

Some corporate resolvers and mobile stacks ignore the time-to-live outright and reach the old address for days. Hence the week.

LEFTOVERS

The lowered time-to-live is itself a leftover, multiplying query volume and query billing on a zone nobody reads.

\$1,900/mo	\$0/mo	100%	10 min	3 days	1 week
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF The weighted record and the managed edge behind it, seven days after full weight, and with them the egress line that was most of the \$1,900.

NEEDS 17 The front door

THE RUNBOOK

- 01 Lower the record's time-to-live to 60 in the authoritative zone a day ahead, then confirm it with dig on several resolvers, not the registrar's view.
- 02 Write the abort criteria as numbers: error rate above a figure, tail latency above a figure, any data-integrity report at all. Name the decider on it.
- 03 Tell the clients a record cannot move: mobile builds with a pinned host, batch jobs holding an old address, third parties allowlisting one.
- 04 Open the change window and freeze deploys with an argocd sync window over it. A release landing mid-shift cannot be told apart from the shift.
- 05 Move the weight to one per cent and soak. Then ten, then fifty, then all of it. The ten minutes in the strip is the last step, not the day.
- 06 Keep the managed edge configured, resolvable and billed at full weight for seven days. Nothing is deleted before the week is out, so the abort stays a field.

ROLLBACK

Putting the weight back returns new connections to the managed edge inside one time-to-live, which is why it was lowered first. That is the whole procedure for seven days. The point of no return is not the weight change but switching the managed edge off when the week is out. If the data failed rather than the traffic, no weight helps and the way back is the database restore.



19 BACKUPS YOU HAVE RESTORED, AND THE PAGER

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
 RUN	MANAGED BACKUP, ALARMS AND A RENTED PAGING SERVICE	 HIGH	IMMEDIATELY

Velero, a continuous database archive and a copy somewhere you are not leaving — then the drill that turns a guessed recovery time into a measured one.

AWS	AWS Backup and CloudWatch alarms	a vault under compliance-mode lock cannot be shortened or removed until its retention expires.
GOOGLE	Backup and DR Service and Cloud Monitoring	a backup vault's enforced retention makes a backup indelible until it expires, by you or by Google, so the copy outlives the decision to leave.
AZURE	Azure Backup and Azure Monitor alerts	a Recovery Services vault protects only resources in its own region, and soft delete holds removed items for fourteen days.

BEFORE YOU START

ACCESS

- An account at an object storage provider unrelated to the cloud you are closing, with object lock
- Five days of one engineer's time for the rebuild drill, on a date nobody may move

SOFTWARE

- velero 1.15 and the Barman Cloud plugin from Move 16, both pinned in the repository from Move 13
- rclone 1.68 for the copy out to the third provider
- Prometheus and Loki with a series budget agreed before the first scrape

PEOPLE

- A named second person behind the escalation, and a rule about what waits until morning

WHY THIS WORKS

Two failures end a company here: the data cannot be got back, and nobody was woken. Schedules are cheap and worthless until somebody has rebuilt from them, so the deliverable is the drill — an estate reconstructed from the repository and the object store while production carries on untouched, with a stopwatch running. That figure is the recovery time objective, and it is usually several times the number in the plan. Monitoring runs on hardware you own; the alerting deliberately does not, because a cluster that has failed cannot report its own failure.

SWAP

If the drill on the spare machine is disruptive, rent a dedicated server by the month and rebuild into that instead.

DO IT FASTER

Make the drill a script, not a document. The second run then takes an afternoon rather than a week.

WATCH OUT

Cluster objects without volume data restore an estate that starts cleanly and holds nothing. Count rows before calling the drill a pass.

LEFTOVERS

Backup vaults bill after the resources they protected are gone, and one under a retention lock stays until it expires.

\$1,100/mo	\$340/mo	69%	0 min	5 days	—
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF Managed backup vaults, their cross-region copies, the alarms and their ingestion, and the rented pager seats — once a restore of your own has been timed and one real page has woken somebody.

NEEDS 16 Postgres, the one that matters 18 Go-live, and how you abort

- 01 | Schedule `velero` nightly for cluster objects, and let the Barman Cloud plugin archive the database from Move 16 continuously, both into the Ceph object gateway built in Move 12.
- 02 | Copy that store out with `nc1one` to a provider that is neither the rack nor the account being closed, with object lock on and append-only credentials, so one identity cannot reach both copies.
- 03 | Do the drill. On the spare machine from Move 06, from the Git repository and those backups alone, build a cluster, restore the database and bring one service up, with nothing touching the original. Time it: that number is the recovery time objective, and the plan that disagrees is wrong.
- 04 | Stand Prometheus and Loki up on your own nodes against the series budget, with drop rules at scrape time. A monitoring bill that outgrows the estate it watches is a cloud habit that follows you home.
- 05 | Put the alerting where the cluster cannot take it down. OneUptime runs the probes, the rota, the escalation and the status page from outside; the author of this book founded OneUptime, and the copyright page says so. Add a dead-man's-switch heartbeat.
- 06 | Write the rota. Three engineers is the minimum that survives leave and illness; most teams here have two. Name the second person, buy a hardware support contract, and record which alerts may wait until morning.

ROLLBACK

Nothing here alters what serves traffic, so backing out is removing two schedules and leaving the managed alarms enabled. The point of no return is the day the provider's vaults age out: after that the only copy of last month is the one you wrote. Keep them until a restore from your own has been timed.



20 CLOSING THE ACCOUNT

CUTOVER

0 MIN



LAYER	LEAVING	RISK	REVERSIBLE
RUN	THE PROVIDER ORGANISATION, ITS AUDIT TRAIL AND ITS SUPPORT PLAN	HIGH	30 DAYS

The estate moved a month ago. The account did not: a dormant organisation still bills, still holds credentials, and still lets someone start an instance in it.

AWS	the management account and its support plan	closing a member account takes the management account, but making one standalone first needs its own contact details, payment method and support plan.
GOOGLE	organisation and its projects	project deletion is scheduled rather than immediate, and a lien refuses the request outright.
AZURE	subscriptions and the Entra tenant	the tenant refuses deletion while any subscription or application registration still exists.

BEFORE YOU START

ACCESS

- Root credentials for the management account, held by two named people
- The registrar login, often held by one person who has since left

SOFTWARE

- aws, gcCloud or az signed in with an identity that can read billing
- rc1one 1.68 or newer to copy the audit trail and billing history somewhere you own

PEOPLE

- Whoever answers the auditor, because the attestations you inherited become yours to produce
- The finance owner who has to see the invoice reach zero and say so

WHY THIS WORKS

A migration that stops at the traffic cutover leaves about \$1,240 a month and a quieter second problem: live credentials, an audit surface someone will still ask about, and enough idle capacity to make drifting back the cheapest decision in the room. Nothing here is deleted until a full billing month has passed with the line at zero and no ticket filed. The failures that follow a migration are monthly rather than daily — the job that runs on the twenty-eighth and cannot find its bucket. Switching off and closing down stay four weeks apart, with everything irreversible on the far side of that gap.

SWAP

Where one thing genuinely has to stay — an archive whose egress you will not pay — move it into a small account of its own and close everything around it.

DO IT FASTER

Begin the key management waiting periods on the first day of the wait, not the last. Seven to thirty days is the AWS range; Google's can be set as long as a hundred and twenty, and a Key Vault holds keys for a retention period fixed when the vault was created. Nothing else waits on any of them.

WATCH OUT

Committed spend does not end when usage does. A Savings Plans commitment keeps billing against the organisation after every resource inside it has gone.

LEFTOVERS

Billing exports, budget alerts and marketplace subscriptions outlive what they were attached to. So does the support plan, which renews on its own anniversary rather than yours.

\$1,240/mo	\$0/mo	100%	0 min	3 days	4 weeks
WAS	NOW	SAVED	CUTOVER	EFFORT	WAIT

TURN OFF The account itself, and with it the support plan, the idle gateways, the log ingestion and the snapshot retention still billing a month after the last user request left. What is left is a platform rather than a project.

NEEDS 18 Go-live, and how you abort 19 Backups you have restored, and the pager

THE RUNBOOK

- 01 Take the final invoice apart with `aws`, `gcloud` or `az`. Expect address translation gateways nothing routes through, CloudWatch log groups still ingesting, snapshots on a retention policy nobody reviews, a support plan priced against spend that has gone, and two subscriptions from a proof of concept three years ago.
- 02 Extract what cannot be recovered later: the audit trail for the period your auditor requires, the billing history, and the compliance attestations you inherited. Copy them out with `rc1one`, then open one of each and check it reads.
- 03 Revisit the archive you decided in Move 15 to leave behind. Data parked in an account you are closing is not archived anywhere. Move it out, or agree in writing to delete it once someone has confirmed nothing still reads from it.
- 04 Move the domain before anything touches identity. Where the registrar sits with the provider — Route 53 is its own, and Azure fronts a partner under its own name — transfer it away, then put the lock back on.
- 05 Turn everything off and remove nothing. Stop the instances, drop the support plan to the free tier, keep the snapshots, and wait one full billing month with the compute lines at zero and no ticket filed. The snapshots and the volumes under the stopped instances go on billing, and are meant to: that residue is what keeps the month reversible.
- 06 Close it from the leaves inward. Federation and human users first, then access keys and roles, then the keys in Secrets Manager or Key Vault, because those decrypt archives you may still hold. Member accounts and subscriptions next; the organisation itself last.

ROLLBACK

Until the closure request this is ordinary work: an account switched off can be switched back on in an afternoon, which is why the wait is four weeks and not four days. The point of no return is the request itself. AWS will reopen a closed account for ninety days, a cancelled Azure subscription keeps its data for thirty to ninety, and a Google project stays scheduled for deletion for thirty — so a restore of anything left inside is possible for thirty days on all three and impossible after ninety. Use the wait to confirm the audit trail and billing history read correctly from your own copies.

A FEW THINGS WORTH KNOWING

None of these is a Move. They are the ten things that make the other 20 work, and most of them are the things people learn in the second year rather than the first.

THE BILL LAGS THE CHANGE BY A MONTH

A resource stopped on the third still bills for the first two days, and a reservation you no longer use bills for a year. Judge a Move by the invoice after next, never by the console.

TWO PEOPLE KNOW, OR NOBODY DOES

The single most common failure mode of a self-run platform is not hardware. It is one engineer who understands the network, and a holiday.

KEEP ONE FOOT IN THE CLOUD ON PURPOSE

An account with a working credential, a Terraform state and a warm standby is not a failure of nerve. It is the cheapest disaster recovery site you will ever have.

WRITE THE RUNBOOK BEFORE YOU NEED IT

Every Move in this book is a runbook because that is the artefact that survives the person who wrote it. A migration that leaves no runbooks behind has to be done again by whoever comes next.

CAPACITY YOU OWN IS CAPACITY YOU HAVE

The cloud taught a generation to treat headroom as waste. On your own metal, idle capacity is the thing that absorbs a bad deploy at four in the afternoon. Buy thirty per cent more than the model says.

HARDWARE FAILS PREDICTABLY AND BORINGLY

Disks, fans, PSUs, optics, in that order, at a rate you can put in a spreadsheet. It is not the drama people expect. The drama is in the change you made on Friday.

THE SAVING IS REAL; THE FREEDOM IS THE POINT

Most teams start this for the bill and finish it for the other thing: being able to answer a question about your own system without opening a support case.

YOU CAN GO BACK

The industry talks about repatriation as though it were one-way. It is not. 0 of the 20 Moves here are genuinely irreversible and the other 20 are not, and knowing which is which is most of the skill.

The best infrastructure decision you make this year will probably be unglamorous, take a fortnight, save a five-figure sum and never be written up anywhere. That is rather the point.

THE BOOK

20 Moves across five stages. 18 cost no downtime at all, 0 cannot be undone, and the whole book executed end to end costs 25 minutes of user-visible outage.

THE TYPE

Set in Archivo, drawn by Omnibus-Type, and JetBrains Mono, drawn by Philipp Nurullin and Konstantin Bulenkov. Both are open source. Every number in this book is set in the mono.

THE NUMBERS

Every price is a public list rate observed while writing, before any discount, and every saving is illustrative of a shape rather than a quotation. Check the arithmetic against your own invoice.

Disclosure: the author founded OneUptime, which this book recommends for alerting, on-call, incidents and status pages. It is recommended because it is Apache-2.0 licensed, self-hostable, and does in one place what that Move would otherwise ask you to assemble from four separate tools. The alternatives named beside it are real ones, and a reader who prefers them loses nothing else in this book.
